

Social Monitoring Report

PUBLIC

Project Number: 55307-001
Semi-Annual Report (October 2023 - March 2024)
May 2024

Bangladesh: Improving Urban Governance and Infrastructure Program

Prepared by the Project Management, Design and Supervision Consultant (PMDSC) for the Asian Development Bank (ADB).

This social monitoring report is a document of the borrower. The views expressed herein do not necessarily represent those of ADB's Board of Directors, Management, or Staff, and may be preliminary in nature. Your attention is directed to the "terms of use" section of ADB's website.

In preparing any country program or strategy, financing any project, or by making any designation of or reference to a particular territory or geographic area in this document, ADB does not intend to make any judgments as to the legal or other status of any territory or area.



Government of the People's Republic of Bangladesh
Ministry of Local Government, Rural Development and Cooperatives
Local Government Division

Local Government Engineering Department (LGED)

Improving Urban Governance and Infrastructure Program (IUGIP)

Semi-Annual Social Safeguard Monitoring Report

(October 2023 - March 2024)

Prepared by:

Project Management, Design and Supervision Consultant (PMDSC)



Development Design Consultants Ltd.



Resource Planning and Management Consultants (Pvt) Ltd.



Design Planning & Management Consultants Ltd.

TABLE OF CONTENTS

	EXECUTIVE SUMMARY	1
I.	INTRODUCTION	4
	A. Project Background	4
	B. Objectives of this SSMR	5
	C. Scope of the SSMR	5
II.	SOCIAL SAFEGUARD IMPACT ASSESSMENT	14
	A. Status of Social Safeguard Program Action Plan (PAP)	15
	B. Program Safeguard Systems Assessment (PSSA)	16
	C. Public Consultation	17
	D. Safeguard Documents prepared in IUGIP	20
III.	INSTITUTIONAL ARRANGEMENTS AND CAPACITY BUILDING	21
	A. Institutional Arrangement for social safeguard	21
	B. Capacity Building and Training for Social Safeguards Compliance	23
IV.	GRIEVANCE REDRESS MECHANISM (GRM)	26
V.	FOLLOW UP ACTIONS, RECOMMENDATION AND DISCLOSURE	29
	A. Mitigation of impacts and GRM management	29
	B. Recommendation	30

TABLES

Table 1: Disbursement-Linked Indicators Output-wise	4
Table 2: Project Pourashavas	6
Table 3: Operation and Maintenance (O & M)- 25 Pourashavas	12
Table 4: Distribution of TMRESC population by Division in Bangladesh	15
Table 5: Safeguard Program Action Plan and status (Social)	16
Table 6: List of public consultations conducted at different Pourashavas during the period of January to March 2024	18
Table 7: Concerns of the participants and responses of facilitators of the public consultations	19
Table 8: Social Safeguard reports prepared for IUGIP	20
Table 9: Status of Recruitment of Resettlement / Social Safeguard Consultants (PMDSC) at PMU Level	22
Table 10: (Chattagram Division): Pourashava-wise Details of Trainees Attended	24

FIGURES

Figure 1: Location of Pourashavas in the Map	13
Figure 2: IUGIP Organogram	23
Figure 3: Grievance Redress System	28

APPENDICES

Appendix 1: Cumulative Physical Progress and Social Impact Assessment up to March 2024	31
Appendix 2: Photo of Public Consultations conducted by Social Safeguards Team in different Pourashavas	76

ABBREVIATIONS

ADB	- Asian Development Bank
PAP	- Project Affected Person
ARIPA	- Acquisition and Requisition of Immovable Property Act
EHS	- Environmental Health and Safety
FGD	- Focus Group Discussion
GOB	- Government of Bangladesh
GRC	- Grievance Redress Committee
GICDC	- Governance improvement and Capacity Development Consultants
GRM	- Grievance Redress Mechanism
LA&R	- Land Acquisition and Resettlement
LGED	- Local Government Engineering Department
LGRD & C	- Local Government Engineering Development and Cooperatives
MDSC	- Management Design and Supervision Consultant
MPR	- Monthly Progress Report
M&E	- Monitoring & Evaluation
PMCU	- Project Management and Coordination Unit
PMDSC	- Project Management Design and Supervision Consultant
PIU	- Project Implementation Unit
PRA	- Project Readiness Assistance
QPR	- Quarterly Progress Report
RCC	- Reinforcement Cement Concrete
R&R	- Resettlement and Rehabilitation
SES	- Socio-economic Survey
SPS	- Safeguard Policy Statements
SPAR	- Sub Project Appraisal Report
SSIA	- Social Safeguard Impact Assessment
TLCC	- Town Level Coordination Committee
TMRESC	- Tribes, Minor Races, Ethnic Sects and Communities

EXECUTIVE SUMMARY

The Asian Development Bank (ADB), Agence Française de Développement (AFD) and Government of Bangladesh (GOB) supported Improving Urban Governance and Infrastructure Program (IUGIP) under the results-based lending (RBL) modality which aim to improve infrastructure facilities such as drains, roads, streetlights, low-income neighborhoods improvements (footpaths, drains, streetlights, tube wells, dust bins and community toilets), and market centers and parks in selected 88 pourashavas. ADB has supported enhancements in pourashavas' service delivery capacity and effectiveness through a series of sector projects to reduce regional disparities and encourage local economic development: the Urban Governance and Infrastructure Improvement Project (UGIIP) in 2002, the second UGIIP (2008), and the third UGIIP (2014).

Under IUGIP, out of these 88 Pourashavas, 63 are classified by LGED as 'mainstream pourashavas' and 25 are under Operation and Maintenance (O & M). 63 Pourashavas were selected for improvement of infrastructure facilities such as construction and improvement work of drains, roads, streetlights, low-income neighborhoods improvements (footpaths, drains, streetlights, tube wells, dust bins and community toilets), market centers and parks under IUGIP. These pourashavas were not selected before for Urban Governance Infrastructure Improvement Projects (UGIIP-i, UGIIP--ii & UGIIP- iii) of LGED. LGED has been considering these pourashavas as mainstream pourashavas. To keep up the continuation of the solid waste management works (SWM) at the pourashava level the completed sub-projects related to SWM under UGIIP-iii further required operation and maintenance (O & M). 25 Pourashavas of this type are included in IUGIP and these Pourashavas are considered for O & M interventions. The project takes a holistic and integrated approach to urban development under the results lending modality. IUGIP is being implemented by Local Government Engineering Department (LGED) under the Ministry of Local Government, Rural Development and Cooperatives (MLGRDC). LGED is the Executing Agency and Pourashavas are the implementing agencies of the Program. IUGIP will follow the Environment and Social Management Framework (ESMF) aligned with the National Laws and ADB safeguards Policy principles for resettlement and Indigenous Peoples/Tribes, Minor races, Ethnic Sects and Communities (TMRESC). IUGIP has commenced on June 2023 and consultants were hired by the PMU through PMDSC with approval from ADB who started their responsibilities and activities since January 2024. This Semiannual Social Safeguard Monitoring Report (SSMR) provides an overview of the Improving Urban Governance and Infrastructure Program (IUGIP) compliance status against the applicable standards, laws and regulations for social safeguard for the period of October 2023 to March 2024. Social screening of the subprojects done using the Involuntary Resettlement Screening Checklist (Appendix 4, ESMF). The Involuntary Resettlement Screening Checklist for TMRESC has been appended as Appendix 2 in this report.

A Program Safeguard System Assessment (PSSA) was conducted and reported on March 2023. During preparation of PSSA due diligence was conducted in five sample Pourashavas to examine RBL program activities. Objectives of the PSSA was to identify potential safeguard impacts and risks and to assess the program systems. The PSSA assessed the existing laws, regulations, rules and guidelines for managing and mitigation of environment and social impacts of the RBL program. The PSSA identified gaps between ADB safeguard Policy Principles and program safeguard systems and recommended programs actions to improve program safeguards and the safeguard action plans.

IUGIP has prepared an Environment and Social Management Framework (ESMF) and submitted to ADB. The key objective of the ESMF is to establish clear procedures and methodologies for environmental and social planning, review, approval and implementation of components to be financed under this Program. The monitoring activities of social safeguard team includes implementation of the ESMF specially for involuntary resettlement and

TMRESC/indigenous peoples safeguard.

The Social Safeguard Team of PMDSC consists of Resettlement/ Social Safeguard Specialist and four Junior Resettlement/Social Safeguard Specialists. The program spans across eight administrative divisions in Bangladesh, with the project *pourashavas* located in each of these divisions. Each Junior Resettlement/ Social Safeguard Specialists is responsible for assessing social safeguard impacts and monitoring of social safeguard activities related to program works in two Divisions under the coordination of Resettlement/ Social Safeguard Specialist. The Resettlement/ Social Safeguard Specialist oversees the performance of four Junior Resettlement/ Social Safeguard Specialists, ensure social safeguards compliance at *pourashavas*/field-level, prepares various periodical social safeguard monitoring reports and implements resettlement plan/ DDRs. Additionally, a Senior Assistant Engineer from PMU serves as the focal person for Resettlement/ Social Safeguard issues.

After design completion, the social safeguards team of PMDSC have visited the subproject sites to assess social safeguards impacts of the project interventions following the prescribed social screening format. During the reporting period, the social safeguard team visited 105 packages across 41 *Pourashavas*. The list of the packages screened by social safeguard team is provided Appendix 1. The team used the 'Involuntary Resettlement Screening Form' (Appendix-2) from the ESMF to identify potential involuntary resettlement impacts and risks. Social safeguard impacts were assessed based on physical observations of the schemes, discussions with community members during public consultations, and interactions with stakeholders, community leaders, and other stakeholders. If the screening identifies involuntary resettlement impacts, LGED will prepare a resettlement plan. For those without involuntary resettlement impacts, due diligence Reports (DDRs) are prepared. During the impact assessments, the social safeguard team conducted 18 public consultations, involving a total of 279 participants, of which 221 were male and 58 were female.

Due Diligence Reports (DDR) were prepared following the assessment of subprojects by the Social Safeguard Teams and submitted to the Team Leader. A draft copy of the DDR has been submitted to Focal Person of Social safeguard designated from PMU. The Focal Person then reviewed the DDR and take action to send it to the ADB for their concurrence. During the reporting period, the Resettlement Team visited 35 *Pourashavas* and prepared 105 DDRs. Out of the 35 visited *Pourashavas*, 34 were visited during PPTA (Project Preparatory Technical Assistance) period of IUGIP. Out of the 105 submitted DDRs 104 DDRs are submitted to PMU during PPTA period. The Resettlement Specialists of PMDSC has been engaged since January 2024.

IUGIP established the grievance redress mechanism (GRM) to voice and resolve social and environmental concerns linked to the project and ensure greater accountability of the project authorities towards all affected persons. The GRM addressed aggrieved persons concerns and complaints promptly using an understandable and transparent process that is gender responsive, culturally appropriate, and readily accessible to all segments of the affected people at no costs and without retribution. A guideline on procedures to operate GRM will be prepared in Bengali and will be mailed to all *Pourashavas* through PMU. The program is still in its very initial stage and Contract Agreement with contractors was furnished for 74 packages and contractor has started their works in 48 packages. The Program beneficiaries and communities have not experienced any construction-related issues. No complaint has been registered by the GRCs during the reporting period.

Capacity building training on environmental and social safeguard policies will be arranged at PMU, PIUs and subproject construction sites. The preparation and implementation of safeguard planning and monitoring instruments will also be discussed in the training program. The guideline on Capacity Building Training for Safeguard Compliance outlined in the ESMF (para 100 – 102).

The training course on gender, environmental and social safeguard, contract management, climate change and quality control of Infrastructure for Contractors and Project Pourashava Engineers is part of the overall training courses designed and implemented aims to capacitate the PMU and PIUs of the program. A capacity -building/ training was arranged during the reporting period at Cumilla Regional Training Centre. 39 participants attended the training from 9 Pourashavas.

I. INTRODUCTION

A. Project Background

1. The Asian Development Bank (ADB), Agence Française de Développement (AFD) and Government of Bangladesh (GOB) supported Improving Urban Governance and Infrastructure Program (IUGIP) under the results-based lending (RBL) modality which aim to improve infrastructure facilities such as drains, roads, streetlights, low-income neighborhoods improvements (footpaths, drains, streetlights, tube wells, dust bins and community toilets), and market centers and parks in selected 88 pourashavas. ADB has supported enhancements in pourashavas' service delivery capacity and effectiveness through a series of sector projects to reduce regional disparities and encourage local economic development: the Urban Governance and Infrastructure Improvement Project (UGIIP) in 2002, the second UGIIP (2008), and the third UGIIP (2014).

2. The RBL program's impacts will be: urban poverty reduced and living conditions improved. The outcome will be: improved municipal services and governance in target pourashavas in terms of increased holding tax collection efficiency (DLI 1) and improved livability (non-DLI). Selected DLIs, identified under each output described below, will create incentives to achieve the program's expected outcome. The program includes the following outputs: Output 1: Institutional capacity for inclusive municipal governance strengthened; and Output 2: Municipal infrastructure improved in quality, access, resilience, and gender responsiveness.

3. The following are the disbursement-linked indicators output-wise:

Table 1: Disbursement-Linked Indicators Output-wise

Indicators	Sub-indicators
Output 1: Institutional capacity for inclusive municipal governance strengthened.	(i) Criteria-based development fund transfer to pourashavas institutionalized (ii) At least 88 pourashavas' governance and planning improved (iii) At least 300 detailed designs of resilient and gender-responsive municipal infrastructure subproject completed (iv) Financial management, and resilient and inclusive planning capacity of LGED improved (v) Gender-responsive operation and maintenance management systems established in 88 pourashavas. (vi) Equity and inclusiveness of women and the poor in at least 88 pourashavas ensured.
Output 2: Institutional capacity for inclusive municipal governance strengthened.	(i) At least 900 km of stormwater drainage rehabilitated or reconstructed (ii) At least 1,500 km of roads rehabilitated or reconstructed. (iii) At least seven climate-resilient and socially inclusive public facilities developed or remodeled.

4. This Semiannual Social Safeguard Monitoring Report provides an overview of the Improving Urban Governance and Infrastructure Program (IUGIP) compliance status against the applicable standards, laws and regulations for Social Safeguard for the period of October 2023 to March 2024. IUGIP has prepared an Environment and Social Management Framework (ESMF) and submitted to ADB. This guiding framework is prepared to ensure that subsequent project activities have a common understanding of the environmental and social issues involved, and a harmonized approach to handling these issues is followed. The ESMF is being used as guidelines to address the safeguard compliances throughout the project area. This social safeguard monitoring report (SSMR) includes the activities during monitoring of implementation ESMF, specifically for involuntary resettlement and Tribes, Minor Races, Ethnic Sects and Communities (TMRESC) safeguards. This SSMR has been finalized based on the site visits under different packages of Pourashavas, it includes discussion with the stakeholders and community people.

B. Objectives of this SSMR

5. As a result-based loan, LGED has to ensure that environmental and social impacts are adequately addressed. The main objective of social monitoring is to: (i) provide an assessment on the progress of social safeguard compliances of the program during the reporting period. This SSMR aims to (ii) provide update/status on the implementation of the ESMF and the safeguards policy action. The key safeguards implementation plans will be the social safeguards documents prepared for the subprojects where involuntary resettlement impacts are triggered; (iii) verify subproject's compliance with social safeguards measures and its progress; (iv) document any issues and concerns in the covered period; and (v) recommend/come up with follow up action to ensure social safeguards compliance.

C. Scope of the SSMR

6. Social safeguard monitoring is an integral component under RBL program. The program will follow the procedures and requirements provided in the Environmental and Social Management Framework (ESMF). At the PMU level, the Social Safeguard Team has developed a methodology following the guidelines of ESMF and appendix 5 of PID for social safeguards monitoring. The Social safeguard experts have been verifying the safeguard compliances with the safeguard measures and its progress toward intended outcomes.

7. Social Monitoring Checklist has been prepared to determine the social safeguard compliances during construction period. It is also to measure the progress/achievement of the indicators from the baseline data generated by the due diligence and social screening exercises at the subproject level. These indicators are essential for monitoring compliance with safeguards during project implementation, with a particular emphasis on involuntary resettlement and TMRESC safeguards. PMDSC consolidates the progress reports and accordingly prepared this SSMR for the RBL program.

8. This semiannual social safeguard monitoring reports are prepared semi-annually following the reporting period October – March and April to September. The program commenced on 1 July of 2023, and the loan became effective on 12 October 2023. This SSMR has been prepared for the period of October 2023 to March 2024.

9. The SSMR aims to:

- (i) Establish and maintain procedures to monitor the progress of implementation of safeguard policies/ plans;
- (ii) Capture any adverse impact in terms of involuntary resettlement impact (income

loss due to loss of access during construction, structure loss, etc.) or TMRESC-related impacts during construction works.

- (iii) Provide information on necessary safeguard methods adopted to avoid, reduce, minimize, mitigate or compensate any adverse impact due to project work.
- (iv) Identify mitigation measures and any residual negative impacts that cannot be avoided,
- (v) Describe process undertaken during project design and to disclose project activities to stakeholders and beneficiaries of the subproject.
- (vi) Describe the subprojects Grievance Redress Mechanism for resolving complaints and its resolution.
- (vii) Monitor and provide recommendation and other follow up actions to ensure progress toward the desired outcome.

10. Project Pourashavas:

Table 2: Project Pourashavas

SI	District	Name of Pourashava	Title of Subproject Package	Component
1	Faridpur	Bhanga	i) IUGIP/BHAN/UT/01/2023 ii) IUGIP/BHAN/UT/02/2023s iii) UGIP/BHAN/UT/02/2023	i) Road (Urban Transport) ii) Road iii) Road
2		Boalmari	i) IUGIP/BOAL/UT+DR/01/2023 ii) IUGIP/BOAL/UT+DR/02/2023 iii) IUGIP/BOAL/UT/01/2023	i) Road + Drain ii) Road + Drain iii) Road
3	Rajbari	Goalanda	i) IUGIP/GOAL/UT+DR/01/2023 ii) IUGIP/GOAL/UT/01/2023 iii) IUGIP/GOAL/MF/01/2023	i) Road + Drain ii) Road iii) Municipal Facility
4	Narayanganj	Araihaazar	i) IUGIP/ARAI/UT+DR/01/2023 ii) IUGIP/ARAI/UT+DR/02/2023 iii) IUGIP/ARAI/UT+DR/04/2023 iv) IUGIP/ARAI/UT+DR/03/2023 v) IUGIP/ARAI/UT+DR/05/2023	i) Road + Drain ii) Road + Drain iii) Road + Drain iv) Road + Drain v) Road + Drain
5	Narshingdi	Monohardi	i) IUGIP/MONO/UT+DR/01/2023 ii) IUGIP/MONO/UT/01/2023 iii) IUGIP/MONO/UT+DR/02/2023	i) Road + Drain ii) Road iii) Road + Drain
6	Munshiganj	Munshiganj	i) IUGIP/MUNS/UT+DR/01/2023 ii)	i) Road + Drain ii) Road + Drain

SI	District	Name of Pourashava	Title of Subproject Package	Component
			IUGIP/MUNS/UT+DR/02/2023	
7	Gazipur	Kaliganj	i) IUGIP/KALI/UT+DR/01/2023 ii) IUGIP/KALI/UT+DR/02/2023 iii) IUGIP/KALI/UT+DR/03/2023	i) Road + Drain ii) Road + Drain iii) Road + Drain
8	Tangail	Madhupur	i) IUGIP/MADH/UT+DR/01/2023 ii) IUGIP/MADH/UT/01/2023 iii) IUGIP/MADH/UT/03/2023 iv) IUGIP/MADH/UT+DR/02/2023	i) Road + Drain ii) Road iii) Road iv) Road + Drain
9	Kishoreganj	Hossainpur	i) IUGIP/HOSS/UT+DR/01/2023 ii) IUGIP/HOSS/DR/02/2023	i) Road + Drain ii) Drain
10	Madaripur	Kalkini	i) IUGIP/KALK/UT+DR/01/2023 ii) IUGIP/KALK/UT/01/2023 iii) IUGIP/KALK/UT/02/2023	i) Road + Drain ii) Road iii) Road
11	Shariatpur	Naria	i) IUGIP/NARI/UT+DR/01/2023 ii) IUGIP/NARI/UT/01/2023 iii) IUGIP/NARI/UT+DR/02/2023	i) Road + Drain ii) Road iii) Road + Drain
12	Gopalganj	Tungipara	i) IUGIP/TUNG/UT+DR/02/2023	i) Road + Drain
13	Munshiganj	Mirkadim	i) IUGIP/MIRK/UT+DR/01/2023 ii) IUGIP/MIRK/UT+DR/02/2023	i) Road + Drain ii) Drain + Drain
14	Gazipur	Kaliakair	i) IUGIP/KALIA/UT+DR/01/2023 ii) IUGIP/KALIA/UT+DR/02/2023 iii) IUGIP/KALIA/UT+DR/03/2023 iv) IUGIP/KALIA/UT+DR/04/2023	i) Road + Drain ii) Road + Drain iii) Road + Drain iv) Road + Drain
15	Kishoreganj	Pakundia	i) IUGIP/PAKU/UT/01/2023	i) Road
16	Kishoreganj	Bhairab	i) IUGIP/BHAI/UT + DR/01 & 02	i) Road + Drain
17	Manikganj	Manikganj	i)	i) Road + Drain

SI	District	Name of Pourashava	Title of Subproject Package	Component
			IUGIP/MANI/UT+DR/01/2023 ii)IUGIP/MANI/UT+DR/02/2023	ii) Road + Drain
18	Netrakona	Madan	i) IUGIP/MADA/UT+DR/01/2023 ii) IUGIP/MADA/UT/01/2023	i)Road + Drain ii) Road
19	Mymensingh	Gaforgaon		
20	Sherpur	Nokla	i) IUGIP/BANS/UT+DR/01/2023 ii) IUGIP/BANS/UT+DR/02/2023 iii) IUGIP/BANS/UT+DR/03/2023	i)Road + Drain ii)Road + Drain iii)Road + Drain
21	Chattogram	Bhanskhali	i) IUGIP/CHAN/UT/01/2023 ii) IUGIP/CHAN/UT/02/2023	i)Road ii) Road
22		Chandanaish	i) IUGIP/SAND/UT+DR/01/2023 ii)IUGIP/SAND/UT/01/2023	i)Road + Drain ii)Road
23		Swandip	i) IUGIP/RAOZ/UT+DR/01/2023 ii) IUGIP/RAOZ/MF/01/2023 iii) IUGIP/RAOZ/UT/02/2023	i)Road + Drain ii) Municipal Facility iii)Road
24		Raozan	i) IUGIP/BRAH/UT+DR/01/2023 ii) IUGIP/BRAH/UT+DR/02/2023 iii) IUGIP/BRAH/UT+DR/03/2023	i)Road + Drain ii) Road + Drain iii) Road + Drain
25	Brahmanbaria	Brahmanbaria	i) IUGIP/BANS/UT+DR/01/2023 ii)IUGIP/BANS/UT+DR/02/2023 iii) IUGIP/BANS/UT+DR/03/2023	i)Road + Drain ii) Road + Drain iii) Road + Drain
26	Chandpur	Faridganj	i) IUGIP/FARI/UT+DR/02/2023 ii)IUGIP/FARI/UT/01/2023	i)Road + Drain ii) Road
27		Matlab(south)	i) IUGIP/MATL/UT+DR/01/2023 ii)IUGIP/MATL/UT+DR/02/2023 iii)IUGIP/MATL/UT/02/2023	i)Road + Drain ii) Road + Drain iii) Road
28	Cumilla	Haziganj	i) IUGIP/HAZI/UT+DR/01/2023	i)Road + Drain ii) Drain

SI	District	Name of Pourashava	Title of Subproject Package	Component
			ii)IUGIP/HAZI/DR/01/2023 iii)IUGIP/HAZI/DR/04/2023	iii) Drain
29	Noakhali	Chowmuhoni	i) IUGIP/CHOW/UT+DR/01/2023 ii)IUGIP/CHOW/UT/01/2023 iii)IUGIP/CHOW/UT/03/2023	i)Road + Drain ii) Drain iii) Drain
30	Lakshmipur	Raipur	i) IUGIP/RAIP/UT/01/2023 ii)IUGIP/RAIP/UT+DR/03/2023	i)Road ii) Road +Drain
31	Feni	Sonagazi	i) IUGIP/SONA/UT+DR/01/2023 ii)IUGIP/SONA/UT+DR/02/2023 iii)IUGIP/SONA/UT+DR/03/2023	i)Road + Drain ii) Road + Drain iii) Road + Drain
32	Bandarban	Bandarban	i) IUGIP/BAND/UT+DR/01/2023 ii)IUGIP/BAND/UT+DR/01/2023 iii)IUGIP/BAND/UT+DR/3/2023	i)Road + Drain ii) Road + Drain iii) Road + Drain
33	Chattogram	Nazirhat	i) IUGIP/NAZI/UT+DR/01/2023 ii)IUGIP/NAZI/UT+DR/02/2023	i)Road + Drain ii) Road + Drain
34	Khagrachari	Khagrachari	i) IUGIP/KHAG/UT+DR/01/2023 ii)IUGIP/KHAG/UT+DR/02/2023 iii)IUGIP/KHAG/UT+DR/03/2023 v)IUGIP/KHAG/UT+DR/04/2023	i)Road + Drain ii) Road + Drain iii)Road + Drain iv)Road + Drain
35	Lakshmipur	Ramgati	i) IUGIP/RAMG/UT/02/2023 ii)IUGIP/RAMG/UT/01/2023	i)Road ii) Road
36	Rangamati	Rangamati	i) IUGIP/BAND/UT+DR/1/2023	i)Road + Drain
37	Noakhali	Bashurhat	i) IUGIP/BASU/UT+DR/01/2023 ii)IUGIP/BASU/UT+DR/02/2023	i)Road + Drain ii) Road + Drain
38	Feni	Daganbhuiyan	i) IUGIP/DAGA/UT+DR/01/2023 ii IUGIP/DAGA/UT+DR/02/2023	i) Road + Drain ii) Road + Drain
39	Lakshmipur	Ramganj	i) IUGIP/RAMG/UT + DR/01 & 02	i) Road + Drain
40	Habiganj	Chunarughat	i) IUGIP/CHUN/UT/01/2023	i)Road

SI	District	Name of Pourashava	Title of Subproject Package	Component
			ii)IUGIP/CHUN/UT+DR/01/2023 iii) IUGIP/CHUN/UT/02/2023	ii) Road + Drain iii)Road
41	Moulvibazar	Kulaura	i) IUGIP/KULA/UT+DR/01/2023 ii)IUGIP/KULA/UT+DR/03/2023 iii)IUGIP/KULA/UT+DR/05/2023	i) Road + Drain ii)Road + Drain iii)Road + Drain
42	Moulovibazar	Moulovibazar	i) IUGIP/MOUL/UT+DR/01/2023 ii)IUGIP/MOUL/UT+DR/02/2023	i) Road + Drain ii) Road + Drain
43	Sunamganj	Chattak	i) IUGIP/MOUL/UT+DR/01/2024	i) Road + Drain
44	Chuadanga	Alamdanga	i) IUGIP/ALAM/UT+DR/01/2023 ii)IUGIP/ALAM/UT+DR/02/2023	i) Road + Drain ii) Road + Drain
45	Kushtia	Bheramara	i) IUGIP/BHER/UT+DR/01/2023 ii)IUGIP/BHER/UT+DR/04/2023 iii)IUGIP/BHER/UT+DR/02/2023 iv)IUGIP/BHER/DR/01/2023	i) Road + Drain ii) Road + Drain iii) Road + Drain iv) Drain
46		Kumarkhali	i) IUGIP/KUMA/UT+DR/01/2023 ii) IUGIP/KUMA/UT+DR/02/2023 iii) IUGIP/KUMA/UT+DR/03/2023 iv) IUGIP/KUMA/UT+DR/05/2023	i) Road + Drain ii) Road + Drain iii) Road + Drain iv) Road + Drain
47	Jashore	Keshobpur	i)IUGIP/KESH/UT+DR/01/2023 ii)IUGIP/KESH/UT/01/2023 iii)IUGIP/KESH/MF/01/2023 iv)IUGIP/KESH/UT/02/2023	i)Road + Drain ii) Road iii) Municipal Facility iv)Road
48	Meherpur	Gangni	i) IUGIP/GANG/UT+DR/01/2023 ii)IUGIP/GANG/MF/01/2023 iii)IUGIP/GANG/UT/01/2023 iv)IUGIP/GANG/MF/02/2023 v) IUGIP/GANG/DR/01/2021	i) Road + Drain ii) Municipal Facility iii) Road iv) Municipal Facility v)Drain
49	Jeshore	Monirampur	i) IUGIP/MONI/UT + DR/01	i) Road + Drain

SI	District	Name of Pourashava	Title of Subproject Package	Component
50	Jhenaidah	Mahespur	i) IUGIP/MOHE/UT+DR/01/2023	i) Road + Drain
51	Lalmonirhat	Patgram	i) IUGIP/PATG/UT+DR/01/2023 ii)IUGIP/PATG/UT+DR/02/2023 iii)IUGIP/PATG/UT+DR/03/2023	i)Road + Drain ii) Road + Drain iii) Road + Drain
52	Kurigram	Ulipur	i) IUGIP/ULIP/UT+DR/01/2023 ii)IUGIP/ULIP/UT/01/2023 iii)IUGIP/ULIP/UT/02/2023 iv) IUGIP/ULIP/UT/03/2023	i)Road + Drain ii) Road iii)Road iv)Road
53	Gaibandha	Sundarganj	i) IUGIP/SUND/UT+DR/01/2023 ii)IUGIP/SUND/UT+DR/02/2023	i) Road + Drain ii) Road + Drain
54	Rajshahi	Bhabanigonj	i) IUGIP/BHAW/UT+DR/01/2023 ii)IUGIP/BHAW/UT/01/2023 iii)IUGIP/BHAW/UT/02/2023	i)Road + Drain ii) Road iii)Road
55		Naohata	i)IUGIP/NAOH/UT/01/2023 ii)IUGIP/NAOH/UT+DR/01/2023 iii)IUGIP/NAOH/UT/02/2023	i)Road ii) Road + Drain iii)Road
56		Bagha	i) IUGIP/BAGH/UT+DR/01/2023	i) Road + Drain
57	Chapainawabganj	Rohanpur	i) IUGIP/ROHA/UT+DR/01/2023 ii)IUGIP/ROHA/UT/01/2023 iii)IUGIP/ROHA/MF/01/2023	i)Road + Drain ii) Road iii) Municipal Facility
58	Pabna	Shanthia	i) IUGIP/SANT/UT+DR/01/2023 ii)IUGIP/SANT/UT/01/2023 iii)IUGIP/SANT/MF/01/2023 iv)IUGIP/SANT/UT/02/2023	i)Road + Drain ii) Road iii) Municipal Facility iv) Road
59	Rajshahi	Charghat	i) IUGIP/CHAR/UT+DR/01/2023	i) Road + Drain
60	Rajshahi	Keshorehat		
61	Naogaon	Nazipur	i) IUGIP/NAZI/UT+DR/01/2023 ii)IUGIP/NAZI/UT+DR/02/2023	i) Road + Drain ii) Road + Drain
62	ChapaiNawabgonj	Shibganj	i) IUGIP/SHIB/UT+DR/01/2023 ii)IUGIP/SHIB/UT+DR/02/2023	i) Road + Drain ii) Road + Drain
63	Bogura	Sariakandi	i)	i) Road + Drain


SI	District	Name of Pourashava	Title of Subproject Package	Component
			IUGIP/SARI/UT+DR/01/2023 ii)IUGIP/SARI/UT+DR/02/2023	ii) Road + Drain

UT = Urban Transport, DR = Drainage

Table 3: Operation and Maintenance (O & M)- 25 Pourashavas

S.I	Division	District	Name of Pourashava
1	Dhaka	Gopalganj	Gopalganj
2		Kishoreganj	Kishoreganj
3		Rajbari	Rajbari
4	Chattogram	Brahmanbaria	Nabinagar
5		Cumilla	Laksam
6		Lakshmipur	Lakshmipur
7	Khulna	Meherpur	Meherpur
8		Chuadanga	Chuadanga
9		Jashore	Benapole
10			Jeshore
11		Magura	Magura
12	Mymenshing	Mymenshing	Muktagacha
13		Netrakona	Netrakona
14		Sherpur	Sherpur
15	Rajshahi	ChapaiNawabgonj	ChapaiNawabgonj
16		Joypurhat	Joypurhat
17		Naogaon	Naogaon
18		Pabna	Bera
19			Ishwardi
20		Sirajganj	Shahjadpur
21	Rangpur	Lalmonirhat	Lalmonirhat
22		Nilphamari	Nilphamari
23		Panchagarh	Panchagarh
24	Barishal	Barguna	Barguna
25		Pirojpur	Pirojpur

Figure 1: Location of Pourashavas on the Map

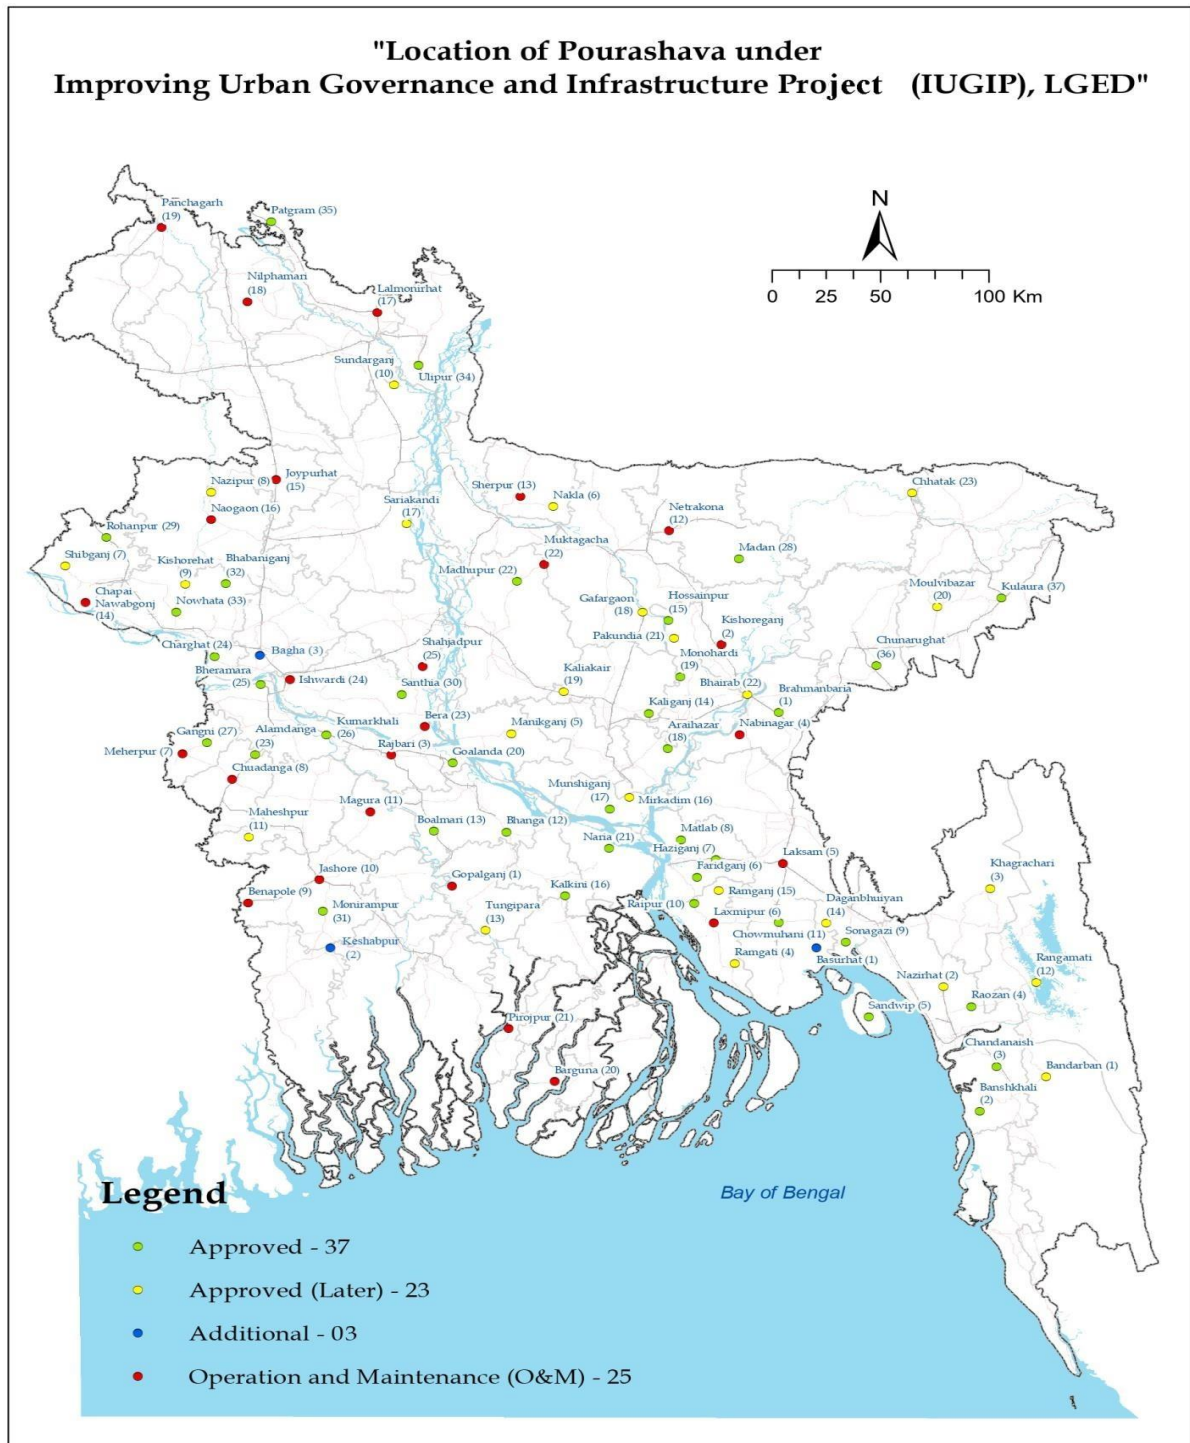

II. SOCIAL SAFEGUARD IMPACT ASSESSMENT

11. Up to March 2024, the social safeguard consultants of IUGIP visited 105 packages at 41 Pourashavas. The consultants screened the social safeguard impacts at the subproject areas. The screening and social assessment process was carried in each scheme using the involuntary resettlement screening checklist provided in the Appendix 4 of the ESMF. From social screening, it was determined whether preparation of Resettlement Plan or Due Diligence report will be required for the packages. As of the reporting period, no project impact assessment has been conducted in any TMRESC(IP) inhabited areas.

12. The Social Safeguard Team has visited the sites upon design completion of the proposed schemes under 105 packages in 41 *Pourashavas* during the reporting period. PMDSC safeguard team along with respective PIUs undertook due diligence of involuntary resettlement impacts in each subproject area and conducted screening of the subprojects using the involuntary resettlement screening checklist provided in the Appendix 4 of the ESMF (Appendix- 2 of this SMR). The team assessed the requirements for preparing the Due Diligence Report. The Social Safeguard Team conducted public consultations and stakeholder meetings as well.

13. Involuntary Resettlement Safeguards. During social screening and due diligence, potential impacts are found mainly related to construction and are short term, localized and can be mitigated with effective construction practices and measures. Roads, footpath and drain works will be carried out along the existing road rights of way within the government lands. Hence, no additional land will be required. Involuntary Resettlement (IR) impacts are not assessed at this stage. However, if any future and/or unanticipated impacts identified during construction involving income loss or displacement the due diligence will be converted to resettlement plan (the list of design completed packages, status of tender award and progress of work has been appended at Appendix No 1).

14. Throughout the implementation period, if any potential resettlement impacts are monitored, necessary mitigation measures will be taken to avoid or mitigate the impacts. Therefore, any potential impact of the subprojects will be fully avoided, and correspondingly, no issues relating to involuntary resettlement will occur during implementation of the subproject. Although, these roads and drainage schemes will not have any involuntary resettlement impact but, the construction/improvement of the subproject may cause only minor and temporary disturbances limited to dust and noise, movement of people etc., which are limited to the construction period only, and could easily be mitigated. Damages/unanticipated losses caused due to construction works will be eligible for compensation following ESMF (Para 77, approved ESMF).

15. Tribes, Minor Races, Ethnic Sects and Communities/Indigenous Peoples Safeguards According to Bangladesh Bureau of Statistics 2011 census data, there are Tribes, Minor Races, Ethnic Sects and Communities (TMRESC) less than 1% (3,693) of total population 1,458,990 in in 37 of 63 *pourashavas* under RBL program. But in two Pourashavas – Banskali and Naohata, TMRESC people are 3.91% (1444 persons) and 1.57% (897) respectively. However, the TMRESC population is scattered around the *Pourashavas* (does not stay in cohesive TMRES communities or groups) in all most all the *pourashavas* and is well assimilated in urban society. Schemes in the two Pourashavas were visited by the consultants of PMDSC and potential impacts were assessed, public consultations with the TMRESC people were organized. No adverse impacts for TMRESC people were identified. Resettlement Specialist, PMDSC joined IUGIP after submission of this SSMR. He will conduct further visits to these two Pourashavas for intensive observation of IP issues.

16. Bangladesh is a country of cultural and ethnic diversity, with over 54 Indigenous/TMRESC Peoples speaking at least 35 languages, along with the majority Bengali population. According to the 2022 census, the country's TMRESC population numbers approximately 1,650,478 which represents 1% of the total population. Chakma, Garo, Manipuri, Marma, Munda, Oraon, Santal, Khasi, Kuki, Tripura, Mro, Hajong and Rakhain are some of the well-known TMRES communities in Bangladesh. TMRESC peoples in Bangladesh call themselves 'Adivasi'.

17. The following table shows the TMRESC population in Bangladesh by Divisions. Pourashavas under the IUGIP (Program) are in all of the eight Divisions of Bangladesh.

Table 4: Distribution of TMRESC population by Division in Bangladesh

Sl.	Divisions	TMRESC total population	Percentage of Total population in the Division (165,158,616)
	National	1,650,159	1.00
1.	Barishal	4,181	0.05
2.	Chattogram	990,860	2.99
3.	Dhaka	82,311	0.19
4.	Khulna	38,992	0.22
5.	Mymensingh	61,559	0.50
6.	Rajshahi	244,592	1.20
7.	Rangpur	91,070	0.52
8.	Sylhet	136,594	1.24

Source: Population and Housing Census 2022, Bangladesh Bureau of Statistics (Table: 2.8).

18. The table describes the total TMRESC population and percentage by Division. It has been revealed from the table that out of the total population in Bangladesh, the TMRESC accounts for 1%. Out of the eight Divisions TMRESC population is less than 1% in five Divisions and slightly higher in two Divisions. The highest percentage (2.99%) of TMRESC people are living in Chattogram Division. The program PSSA describes out of 86 Pourashavas in 37 Pourashavas under the RBL program the TMRESC constitutes less than 1% of total population but at two pourashavas TMRESC population is 3.91% and 1.57% at Banskali and Naohata respectively. In case of males and females of TMRESC, the ratio is 1.01% and 0.99% respectively.

19. The program will prepare TMRESC Plan, if required, following the policy principles outlined in ESMF. The safeguard document will contain a specific action plan for beneficial impacts of TMRESC.

20. The project is assessed category B for indigenous people/ Tribes, Minor Races, Ethnic Sects and Communities (TMRESC). However, the TMRESC population is scattered around the Pourashavas in almost all the Pourashavas and are well assimilated in urban society.

21. In case of involuntary resettlement and TMRESC impacts are assessed, the program will prepare resettlement plan and TMRESC Plan following the policy principles outlined in ESMF.

A. Status of Social Safeguard Program Action Plan (PAP)

22. The following program actions are suggested to mitigate the identified risks and strengthen the capacity of LGED to implement the RBL program:

Table 5: Safeguard Program Action Plan and status (Social)

Actions	Responsible Agency	Time Frame for implementation	Status of safeguards PAPs
1. Establish and operationalize environmental and social management framework (ESMF) for the RBL program and ensure compliance	LGED Pourashavas	Mar 2023 (Developed) Operationalized (implementation period)	ESMF Developed and operationalized and will continue during project implementation period
2. Social Safeguard focal persons or specialists are assigned to LGED Program Management Unit, and pourashavas to strengthen the coordination for environmental and social safeguards compliance. a. Appoint dedicated social safeguards staff at PMU and build capacity to implement ESMF b. Appoint safeguards staff in PIUs and build capacity for implementation of RBL program activities in compliance with ESMF	LGED Pourashavas	Mar/ July 2023	Resettlement/ Social safeguard Specialist Joined in July 2024 and 4 Junior Resettlement/ Social safeguard Specialists joined by February 2024 at PMU. One Senior Assistant Engineer of LGED has been assigned as a Focal person for Social Safeguard since January 2024. Pourashavas assigned one person for safeguard issues.
3. Model for social safeguards compliance with respect to market development under Third UGIIP adopted and operationalized.	LGED Pourashavas	July 2023 (adopted) July 2023-June 2028 (Applicable to any market development under the RBL	Social Screening was done for 7 Market Centers during PPTA period. No Work Order issued for market development up to March 2024. Model for social safeguards compliance with respect to market development under Third UGIIP adopted and is operationalized
7. Include a specific action plan for the effective participation of Tribes, Minor Races, Ethnic Sects, and Communities (TMRESC) (if any) in the design of proposed infrastructures in applicable social safeguards documents and ensure their inclusion in the program benefits.	LGED Pourashavas	July 2023–June 2028	Preparation of Action plan for the effective participation of Tribes, Minor Races, Ethnic Sects, and Communities (TMRESC) (if any) is under process. The Action Plan will be included in the next SSMR.
8. Semi-annual reporting on implementation of environmental and social safeguard program actions.	LGED	Semi-annual during implementation	Semi-annual Social safeguard Monitoring Report (Oct.2023 to March 2024) prepared and submitted to ADB

B. Program Safeguard Systems Assessment (PSSA)

23. A Program safeguard Systems Assessment (PSSA) was conducted for the program. Based on the ESMF, at that time, due diligence was done in five program towns (Chowmohani, Rouzan, Araihasar, Naohata and Keshabpur). During the assessment, the team physically

visited the Pourashavas and no IR potential impacts of project construction works related to involuntary resettlement were identified. For Chowmohani, a proper due diligence will be undertaken and accordingly, appropriate social safeguards documents will be prepared and/or updated. Several stakeholder consultation meetings were conducted with the Mayors, Panel Mayors, Pourashava Councilors and Secretaries, TLCC and WC Members, concerned Engineers and Officials of the Pourashavas. Public consultations in these Pourashavas were also conducted to exchange views with the beneficiaries of the program, disclosed project objectives and activities and also assess the potential impacts of the program.

24. It has been reported in the PSSA that people from Tribes, Minor Races, Ethnic Sects and Communities (TMRESC) are less than 1% of total population. But at Naohata and Banskali (out of the sample Pourashavas) people of TMRES Communities are 1.57% and 3.91% of total population of the Pourashavas respectively. It was reported in the PSSA report that, "However, the TMRESC population is scattered around the Pourashavas (does not stay in cohesive TMRES communities or groups) in all most all the pourashavas and is well assimilated in urban society."

25. The social safeguard team visited the subproject areas and conducted meeting with the community people and separately with TMRESC people. No significant adverse impact was reported neither from mainstream people nor from TMRESC people. Some impacts found which were short term and mitigated with good construction practices. The beneficial impacts on community people are recorded from the feedbacks from participants. It was reported from the project beneficiaries that after completion of the road travelling and carrying goods will be comfortable, easier, time saving and also economic.

26. The Resettlement/Social safeguard Specialist plans to visit the three Pourashavas (Banskali, Naohata and Chowmohani) along with Environmental Specialist, Jr. Resettlement Specialists to engage with the community people. The program has been delayed due to some unavoidable reasons and devastating floods in the concern areas.

C. Public Consultation

27. Public consultations with the community people at different subprojects of Pourashavas were undertaken to exchange views on subproject implementation and to disclose project activities. The public consultations are conducted with prior notice, ensuring wide reach and accessibility for individuals from various sectors. At project implementing unit, (PIU), contractors with the supervision of the Pourashavas are implementing construction works of road, drain and streetlight under different schemes. Participants of these consultations are community people, Pourashava officials, Councilors, TLCC, WC members, People's Representatives, contractors or their representatives, local leaders, businessmen, religious leaders, journalists, other government officials and different stakeholders since subproject preparation to date who participated at different stages of the project activities. The consultations/meetings were conducted at subproject sites and Pourashava offices. In addition, hotspot/information discussion were held in the project site as a part of information dissemination about the upcoming subproject. Details on consultation/meetings are described in the following paragraph and in Table No. 2. IUGIP arranged 18 public consultations in 7 Pourashavas during the reporting period. A total of 279 participants (male- 221 and female-58) participated in the meetings. The major objective of such consultations was to exchange views on project objectives and activities, assessing potential impacts of project activities and to disclose project mitigation plan of potential adverse impacts. In these meetings different issues related to project activities, problems/constraints and project methods to address the constraints are identified and discussed. Consultation is a continuous process which requires holding meetings with the project beneficiaries from the very beginning of the project

preparation to the stages of implementation and monitoring of the project activities. The Grievance Redress Mechanism of the project has been discussed in these meetings. Formation of grievance redress committees (GRCs), GRC functions, types of complaints, procedures of submitting complaints, different stages of GRM etc. were discussed at the meetings. Feedback from the participants are recorded and facilitators (Resettlement Team) responded on the concerns of participants. List of public consultations held during the reporting period are showed in the following table and concerns raised by the participants are discussed in the following paragraph. The community people, local leaders, project beneficiaries along with subprojects and other stakeholders attended the public consultation. This interactive approach will continue during the implementation of the subproject. The findings of the above consultations revealed lots of positive impacts despite a few temporary impacts/concerns limited to construction period only, which have the scope of mitigation.

Table 6: List of public consultations conducted at different Pourashavas during the period of January to March 2024

Sl.	Date	Pourashava	Venue	Participant		
				Male	Female	Total
1.	30.01.2024	Kaliakair	Ward Councilor's office	10	0	10
2.	30.01.2024	Dagunbhyuan	South Jagatpur	16	17	33
3.	30.01.2024	Mirkadim	Sudarchar Template	9	6	15
4.	01.02.2024	Mirkadim	Beside of Ghuangola Mosque	15	0	15
5.	03.03.2024	Nazirhat	East Farhadabad	13	2	15
6.	03.03.2024	Sariakandi	Girls' School Moor	16	2	18
7.	03.03.2024	Sariakandi	Dakhin Hindukandi	14	4	18
8.	04.03.2024	Nazirhat	Pourashava Office	13	2	15
9.	04.03.2024	Sariakandi	Shapara	14	4	18
10.	04.03.2024	Sariakandi	Police Line Road	15	3	18
11.	05.03.2024	Dagunbhyuan	Badarpur	10	5	15
12.	05.03.2024	Sundargonj	Mirgonj Bazar	15	2	17
13.	06.03.2024	Sundargonj	Bamonjol	15	2	17
14.	06.03.2024	Chatak	Boula Bondara Para	8	3	11
15.	06.03.2024	Chatak	Labor Para	6	5	11
16.	06.03.2024	Chatak	Front side of Poura Auditorium	11	-	11
17.	07.03.2024	Chatak	Nowarai Road	10	1	11
18.	07.03.2024	Chatak	Koma Bashkhal Mour	11	-	11
Total participants				221	58	279

28. The following topics were discussed in public consultations. The topics may be summarized as follows:

- (i) Briefing on Project background and objectives in short.
- (ii) Background of subproject selection and scope of the construction works.
- (iii) Potential benefits from the subproject expected by the program.
- (iv) Potential problems may occur during construction and their level. How those will be avoided or mitigated by the PIU and contractors.
- (v) Project policy on social safeguard, responsibility of PMU, PIU and contractors to address the social safeguard compliances.
- (vi) Project Grievance Redress Mechanism in details was discussed. The focal person of GRC in PIU, contractors' responsibility in GRM, and process of grievance hearing was discussed.

- (vii) Copy of Grievance Registration Form was shown to the attendance.
- (viii) Suggestions from the beneficiaries for the betterment of the subproject invited.
- (ix) Requirement of acquisition for the subproject was discussed.
- (x) Responsibility of beneficiaries in well maintenance of the subproject discussed

29. During the public participation, the participants exchanged their views with the facilitators. The participants expressed their concerns too. Concerns of the participants of the public consultations are mostly common. Concerns of the participants and responses of facilitators of the public consultations are mentioned in the following table.

Table 7: Concerns of the participants and responses of facilitators of the public consultations

Sl. No.	Concerns of the participants	Responses of the facilitators
1.	When the subproject works will be completed?	The completion date and up to date progress of the subprojects were disclosed.
2.	Is it possible to complete the subproject works earlier?	Contractors discussed on possibility of completion of the subproject works before the completion date. If there were constraints to complete the work in due time it was also discussed.
3.	Do the PIUs control the quality of construction materials.	Mainly quality of the construction works is controlling by PIUs. There is one Monitoring Engineer (ME) from PMDSC at each program Pourashavas. The PIU Engineers and ME of PMDSC jointly controls the quality of construction works at field level. The Upazila level and District Level LGED contribute in maintaining quality of works. There are Quality Control Engineers at PMU. They also monitor the quality of the subproject construction works. The construction materials are tested mainly at the laboratories of nearest Public Engineering Universities and LGED laboratories.
4.	How people can submit their complaints on construction works if they have and how the complaints will be addressed by the program?	The project GRM was discussed. The participants were informed that there are Complaint Box and Complaint Registers at Pourashava offices. Any aggrieved person can submit their complaints at Pourashavas in written, by mail, by email, by post or through telephone. They also can submit their complaints at Contractors office or by writing complaints in Complaints register at Contractors office. Hearing of their complaints are arranged in presence of complainants. Complainants have the scope to appeal to higher GRCs if they are not satisfied with the decision of 1 st level GRCs. They can also submit their complaint to the upper level GRCs and finally to Complaint Receiving Officer (CRO) at ADB Headquarters or the ADB Bangladesh Resident Mission (BRM).
5.	Whether land acquisition will be required? If required how it will be compensated.	The program construction works are carried out on existing RoWs on Pourashava lands. So, land acquisition will not be required. At the early stage of subproject design, social impacts are screened. If any IR or TMRESC impacts are assessed, an RP or TMRESC plan will be prepared. Compensation will be provided following requirements in the ESMF.

Sl. No.	Concerns of the participants	Responses of the facilitators
6.	Request to complete the construction works before rainy season.	In response to participants concern to complete the work before rainy season, the possibility or the real situation were discussed in the meetings.
7.	How the movement of overloaded trucks will be controlled on the subproject roads?	Existing traffic rules will be followed for the subproject. Supervision of the community people will help to control movement of overloaded transports on the subproject roads.
8.	Whether the drains will be covered with slabs?	The under-construction drains will be covered with slabs.
9.	How the clogging/blockage of the drains will be removed?	The designated PIU workers will work to maintain the flow of the drains. The participants were also requested not to throw any solid waste in the drains.
10.	Where will be outfall of the drains?	The outfalls were shown in the design.
11.	What will be the lighting facilities of the constructed roads during night?	Electric lights/ solar lights will be provided according to sub-project design.
12.	Have there any scope to work for the local female workers? Whether their wage will be equal to male workers.	The female workers are always welcome to work. They will be equally paid as the male workers are receiving for same kind of work.

D. Safeguard Documents prepared in IUGIP

30. IUGIP has been implementing the program in a transparent way. A list of Safeguard documents has been prepared under the IUGIP to ensure the disclosure of project information related to project activities to the project beneficiaries, Government Agencies of Bangladesh and ADB.

Table 8: Social Safeguard reports prepared for IUGIP

S. No.	IUGIP Social safeguard reports	Stage of preparation	Disclosed on ADB Website	Disclosed on LGED Website	Comments
1.	Program Social Safeguard Assessment (PSSA)	Prepared and submitted to ADB.	https://www.adb.org/sites/default/files/linked-documents/55307-001-pssaab.pdf	https://iugip-lged.org/document_archive/uploads/PSSA.pdf	
2.	Environmental and Social Management Framework (ESMF)	Prepared and submitted to ADB.	https://www.adb.org/sites/default/files/project-documents/55307/55307-001-pam-en.pdf	https://iugip-lged.org/document_archive/uploads/ESMF%20final%2023%2006.%202024(time12.03pm)-further-updated-	

S. No.	IUGIP Social safeguard reports	Stage of preparation	Disclosed on ADB Website	Disclosed on LGED Website	Comments
				05Jul2024.pdf	
3.	Due Diligence Report	Prepared and submitted to PMU			All the DDRs cleared by PMU. These will be disclosed in February, 2025.
4.	Semi-annual Social Safeguard Report	Prepared and submitted to ADB.			SSMR-1 (Oct 23 to Mar. 24) submitted to ADB for review,

31. Since mobilization at the initial stage, the PPMDSC and Social Safeguard Specialists have been working on to finalize the design and preparation of required social safeguard documents/ reports for the identified subproject as well as conducting of feasibility study and worked closely with PMDSC during preparation of final design for the new subprojects selected. During the reporting period, the safeguard consultants subsequently also prepared number of social safeguard reports for subprojects with the design-completed schemes.

32. A list of schemes under different Packages visited and impact assessed by the. Social Safeguard Team of PPMDSC is appended at Appendix- 1. The roads and drains will be constructed within the rights of way (ROW) of Pourashava roads. Due diligence was conducted to assess the schemes. The assessment indicates that there will be no land acquisition or physical displacement or permanent economic displacement of any individual, household or community.

III. INSTITUTIONAL ARRANGEMENTS AND CAPACITY BUILDING

A. Institutional Arrangement for social safeguard

33. The Ministry of Local Government, Rural Development and Cooperatives (MLGRDC) acting through its Local Government Engineering Department (LGED) is the Executing Agency. At the LGED, PMU has been established and this PMU is being supported by the consultants. At the *Pourashava* level, district level team of LGED (PIU) will implement the program related construction works. As part of current RBL program implementation, the PSSA has recommended as an action point for recruitment of one Environmental Safeguard Specialist and one Social Safeguard Specialist at the PMU level. Both safeguard specialists are reporting to the Project Director and together and formed the safeguard cell. At PIU level, one officer of Assistant Engineer rank is designated as safeguard focal person, who will ensure EMP and Resettlement Plan implementation. Project Management, Design and Supervision Consultants (PPMDSC) are engaged to work closely with and advise the PMU and PIUs.

34. Social Safeguard Team of PPMDSC constitutes of Resettlement/ Social Safeguard Specialist and four Junior Resettlement/ Social Safeguard Specialists. Responsibility of Social Safeguard Specialist is to determine requirement of preparation of RP or DDR and to prepare them according to requirement in compliance with ADB SPS 2009 and Regulations of GoB. The team has been confirming inclusion of DDRs in bidding documents and civil work contracts, has been monitoring the implementation and disclosing of social safeguard (DDR)


Plans and Grievance Redress Mechanism. The social safeguard team consolidates monthly social safeguard from PIUs and to prepare and disclose in Semi-annual and Annual Social Safeguard reports upon approval of ADB. PMU Safeguard Cell will assess training need and coordinate training activities for PMU and PIUs officials, Contractors.

Table 9: Status of Recruitment of Resettlement / Social Safeguard Consultants (PMDSC) at PMU Level

Position	Joining Date	Leaving Date	Present status
Resettlement/ Social Safeguard Specialist	1 July, 2024	-	Working
Jr. Resettlement/ Social Safeguard Specialist-1	January, 2024	-	Working
Jr. Resettlement/ Social Safeguard Specialist-2	January, 2024	-	Working
Jr. Resettlement/ Social Safeguard Specialist-3	February, 2024	-	Working
Jr. Resettlement/ Social Safeguard Specialist-4	February, 2024	-	Working

35. Municipal Engineers are deployed by PPMDSC at all Pourashavas selected for the program. They assist Pourashavas in preparation of Development Plan (PDP) meeting all necessary requirements including social and environmental safeguard issues followed at Pourashava level.

Figure 2: IUGIP Organogram

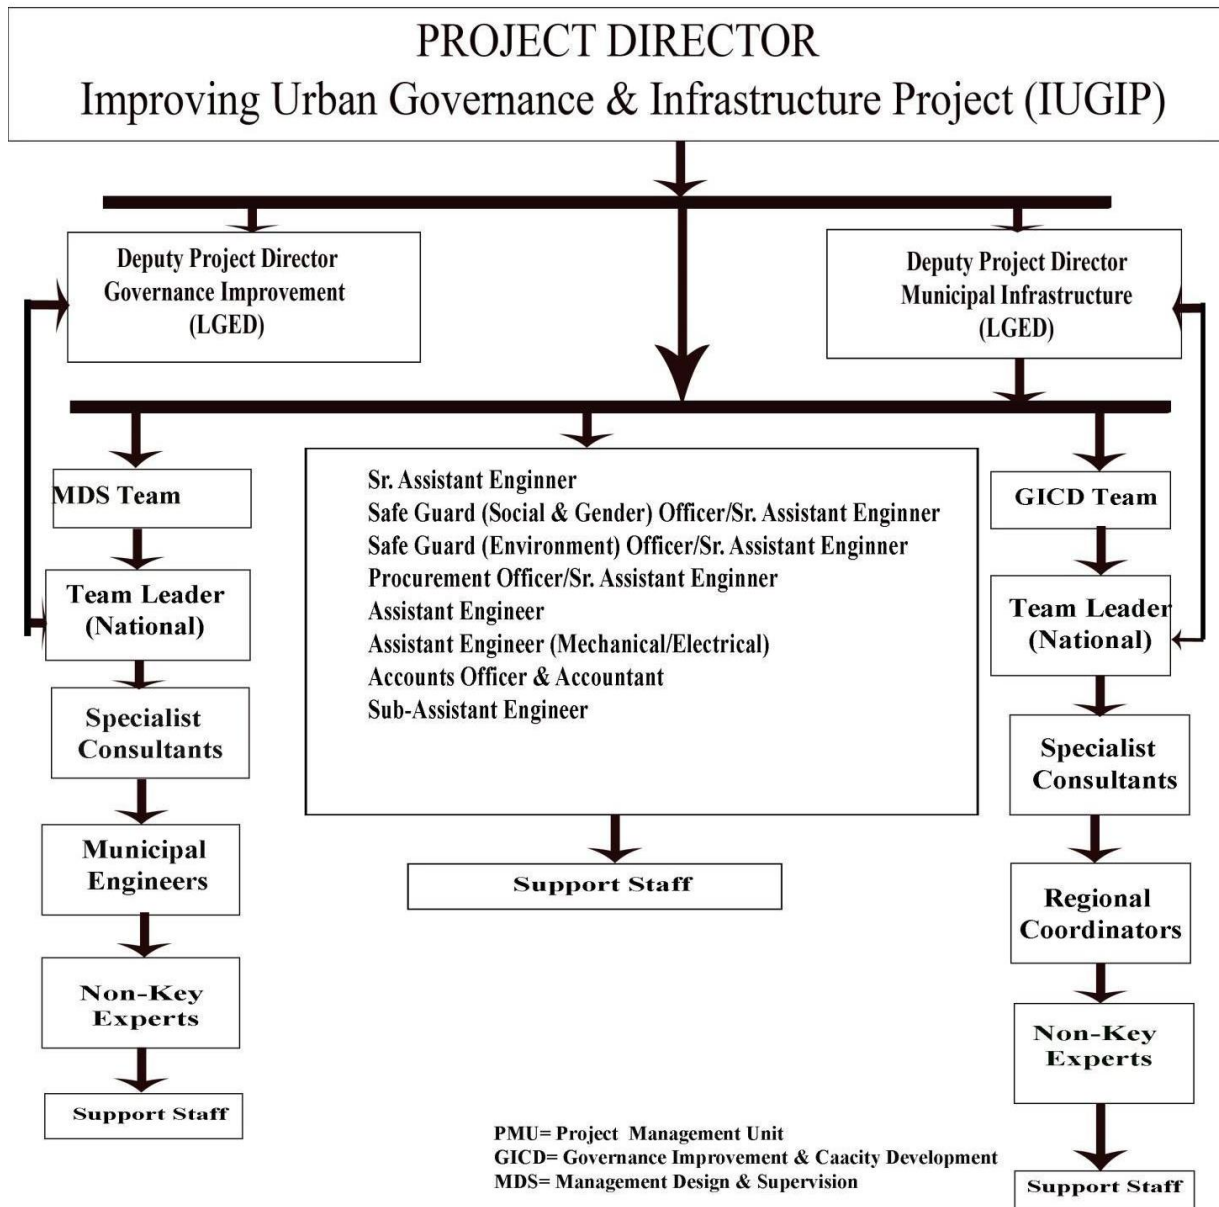

B. Capacity Building and Training for Social Safeguards Compliance

36. Capacity building training on environmental and social safeguard policies will be arranged at PMU, PIUs and subproject construction sites. The preparation and implementation of safeguard planning and Monitoring instruments will also be discussed in the training program. A guideline on Capacity Building Training for Safeguard Compliance outlined in the ESMF (para 100 – 102).

37. The Training course on 'Gender, Environmental and Social Safeguard, Contract Management, Climate Change & quality Control of Infrastructure for Contractors and Project Pourashava Engineers' constitutes a part of the overall training courses designed and implemented in line with the Objectives of the Capacity Development of MDS under Improving Urban Governance and Infrastructure Project, Local Government Engineering Department. A

Capacity Capacity building training was arranged during the reporting period at Cumilla Regional Training Centre. 39 participants attended the Course from 9 Pourashavas.



Mr.Md.Mostafa Hasan, SE, LGED,Cumilla Region is seen to inaugurate the training session on Gender, Environmental & Social Safeguard, Contract Management, Climate Change & quality Control of Infrastructure for Contractors and Project Pourashava Engineers'held on 10 March, 2024 at RTC-Cumilla. JR. Resettlement Specialist, PMDSC, IUGIP was present as a Resource person in the program.

38. The overall objective of this training course is to enhance knowledge, skill and positive change of attitude specially of technical officials of Pourashavas, Contractors and IUGIP officials in order to fulfilling the criterion of the development partners' requirements efficiently.

39. The following table shows the name of the Pourashavas, category and number of participants attended in the daylong training.

Venue: RTC, LGED, Cumilla

Date:10 March,2024

Batch: 01

Table 10: (Chattagram Division): Pourashava-wise Details of Trainees Attended

Sl. No.	Name of Pourashavas	Category and Total Number of Trainees Participated				
		XEN/AE/SAE(PIU)	AE (IUGIP)	ME (IUGIP)	Contractors/Cont. Representative	Total
1.	Raipur	1	1	1	1	4
2.	Khagrachhari	1	1	1	3	6
3.	Matlab	1	1	1	2	5
4.	Banskhali	1	0	1	2	4
5.	Brahmanbaria	1	1	1	2	5

Sl. No.	Name of Pourashavas	Category and Total Number of Trainees Participated				
		XEN/AE/SAE(PIU)	AE (IUGIP)	ME (IUGIP)	Contractors/Cont. Representative	Total
6.	Hagiganj	1	1	1	1	4
7.	Chowmuhani	1	1	0	2	4
8.	Sonagazi	1	0	1	1	3
9.	Sandwip	1	1	1	1	4
Total :		9	7	8	15	39

Note: XEN = Executive Engineer, AE =Assistant Engineer, SAE =Sub-Assistant Engineer, ME= Municipal Engineer

Note: In all,24 technical officials and 15 Contractors were imparted training. The number of trainees invited was 43 and attended 39. Percentage of attendance was **90.70%** and achieved trainee-days was **39**.

40. The Resettlement/ Social safeguard Specialist joined the Program on 1 July, 2024. So, one Junior Resettlement/ Social safeguard Specialist attended the training program. The Social Safeguard policy of the program was discussed. To address the project social safeguard compliances in project works responsibility of concerned persons were discussed. The preparation of Social Safeguard Periodical Reports and advised to mitigate or avoid adverse impacts were also discussed.

41. Social safeguard Capacity Building Training will be arranged for PMU Officials, PIU Officials of 63 Pourashavas and for contractors awarded contracts for construction works. Project Safeguard Policies (Environment and Social) as outlined in ADB SPS 2009, EMP and Implementation of Resettlement Plan will be discussed in the training. The project GRM, social safeguard monitoring requirements and mitigation measures will be oriented during the training program. As a part of capacity building during the implementation of IUGIP RBL Program, training program will be conducted at PMU, PIUs and subprojects construction sites.

42. Preparation of training plan and training materials are under process. It is expected that the Capacity Building Training will be conducted in September and October of 2024. Resettlement/ Social Safeguard Specialist, Environmental Specialist are preparing the training material and will conduct the training program. The Jr. Resettlement/ Social Safeguard Specialists and Jr. Environment Specialists will also be included as trainer. Environment Specialist and Jr. Environment Specialist will train the participants on project environmental safeguard policies. The Project Safeguard policies are being prepared following the ADB Safeguard Policy Statement 2009 and on GoB Safeguard Policy. The training will be arranged on a regular interval. Progress of the capacity building training will be reported to ADB time to time.

IV. GRIEVANCE REDRESS MECHANISM (GRM)

43. In order to receive and facilitate the resolution of affected people's concerns, complaints, and grievances concerning the subproject's safeguards performance, IUGIP has established a Grievance Redress Mechanism (GRM) consistent with the ESMF.¹ This GRM will work to address any complaints related to project activities that arise during the implementation of the subproject. The RBL program have both online as well as offline mode to receive the grievances. An aggrieved person can register his/her complaint through telephone, mobile, or email or by writing in the Complaint Registers maintaining in the PIU/Pourashava office and contractor's offices.

44. Complaint boxes are installed at all of the PIUs. The safeguard focal person at PMU will ensure the follow-up of the grievance until resolved. The PMU will have a regular review to ensure that all grievances are resolved in time-bound and through a transparent mechanism. The affected person is free to access the country's legal system at any time and at any stage. The affected person also can use the ADB Accountability Mechanism (AM) through directly contacting (in writing) the Complaint Receiving Officer (CRO) at ADB headquarters or the ADB Bangladesh Resident Mission (BRM). The sample of Grievance Registration Form has been appended in Appendix- 4. The Registration Form used in ESMF has been revised following the requirement and the English version of the form annexed in this report. PMU safeguard officer will have the overall responsibility for timely grievance redressal on environmental and social safeguards issues and for registration of grievances, related disclosure, and communication with the suggested party through the PIU designated safeguard focal person.

45. The GRCs are using Grievance Redress Registers to maintain the records of complaints and of resolution of complaints. The Grievance Redress Registers recorded summary of the complaints, hearing processes of complaints, GRC decision and opinion of the complainants. A guideline to operate GRM, sample of Grievance Registration Form and model of Grievance Registers will be prepared in Bengali and sent to all of the project Pourashavas for their uses.

46. The multi-tier GRM for the project is outlined below. Time-bound schedules of each tier discussed and persons responsible for arranging hearing and redressing the complaints are also identified.

47. **1st Level Grievance, Pourashava Level PIU.** The contractors, PIU Safeguard and Gender Focal person can immediately resolve issues on-site or at Pourashava level in consultation with each other with the support of Administrative Officer of Pourashava, designated municipal ward councilor and will be required to do so within 7 days of receipt of a complaint/grievance. Assistance of ward committees (WC) will be sought if required for resolution of the issue, by any one or all of them jointly. The First Level Grievance Redress Committee will be comprised of the following members:

- a. Chief Executive Officer or Paura Nirbahi Officer
- b. Executive Engineer, Pourashava/ Safeguard and Gender Focal person
- c. Administrative Officer, Pourashava (will act as secretary GRC level-1)
- d. Municipal Ward Councilor (designated)/ WC member
- e. Medical Officer/Environment Health Safety (EHS Supervisor)/, Contractor
- f. Affected Person's Representative/ Community or NGO Representative of project Area.

48. Some designation of the members of GRC required to be changed in ESMF

49. **2nd Level Grievance, Pourashava Level.** All grievances that cannot be redressed within 7 days at Ward level will be brought up to the Second Level Grievance Redress Committee (GRC) headed by the Panel Mayor. Second Level Grievance Redress Committee at Pourashava level will attempt to resolve the grievance /complaint within 15 days. The composition of 2nd level Grievance Redress Committee is as follows:


- (i) Panel Mayor of the Pourashava
- (ii) Chief Executive Officer/ Paura Nirbahi Officer (will act as member secretary)
- (iii) Executive Engineer of the Pourashava
- (iv) Concerned Councilor of the Pourashava
- (v) Administrative officer of the Pourashava
- (vi) One women member/ Reserve women seat councilor
- (vii) Representative of Affected Person/ TLCC member/ NGO member

50. **3rd Level Grievance, Project Management Unit (PMU):** The grievances that are not redressed within 30 days of submission at Pourashava level will be forwarded to the PMU level. Pourashava Level Grievance Redress Committee will refer any unresolved or major issues to the PMU level Grievance Redress Committee, which will be headed by the Project Director and will have Mayor of the Pourashava, Deputy Project Director, Senior Assistant Engineer, Resettlement/ Social Safeguard Specialist, Environment Specialist as Committee Members. The 3rd Level Grievance Redress Committee will resolve the complaints/grievances within 30 days of receiving. The 3rd Level/ PMU level Grievance Redress Committee will comprise of:

- (i) Project Director,
- (ii) Mayor of the Pourashava
- (iii) Deputy Project Director
- (iv) Senior Assistant Engineer (will act as Member Secretary GRC level-3)
- (v) Resettlement/ Social Safeguard Specialist
- (vi) Environmental Specialist
- (vii) Senior Assistant Engineer / Gender Focal Persons

51. (At present (September 2024) position of Mayors and Counselors are abolished. Government deployed Executives for the position of Mayor. So, the Executive are replaced in place of Mayor in GRCs and Representatives of Executive will be replaced in position of Councilor in GRCs)

Figure 3: Grievance Redress System

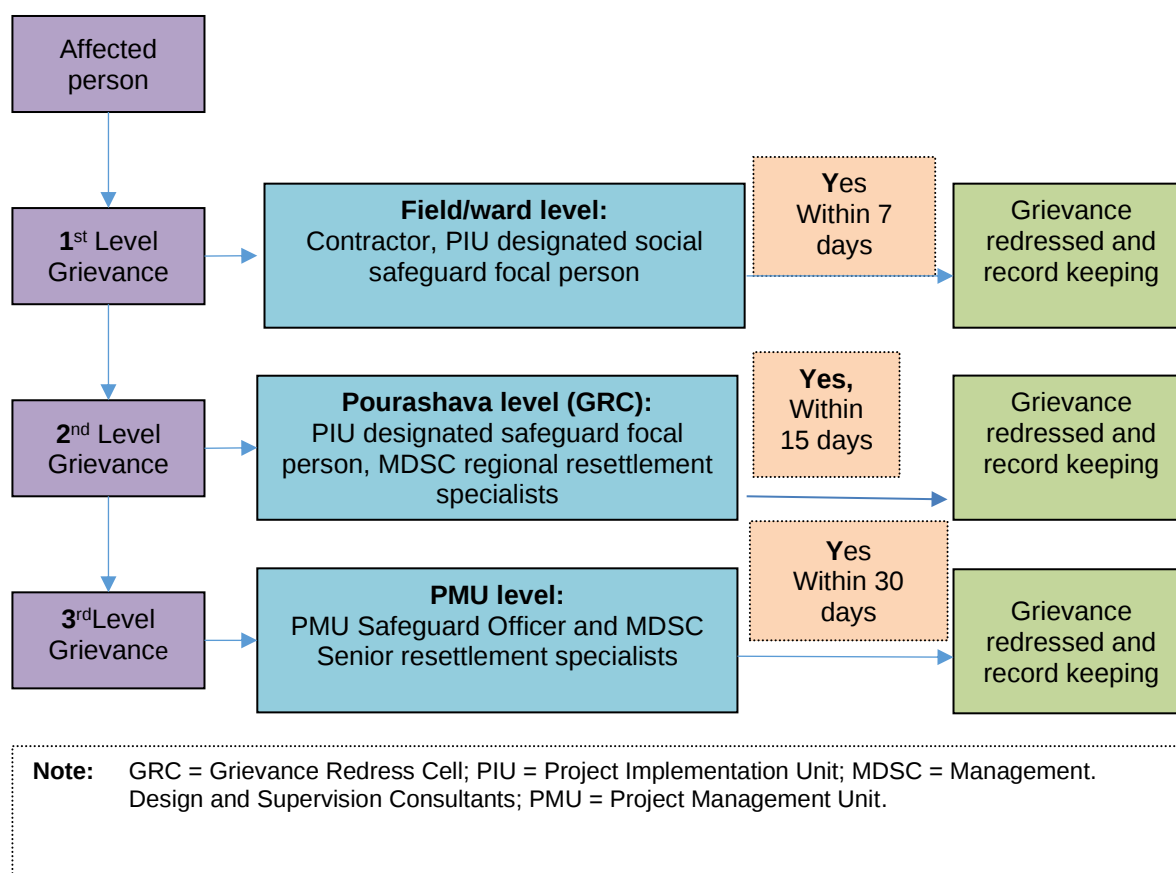

52. As the reporting period is very initial stage of the project, project development activities still have not started at most of the sub-projects, the project beneficiaries still do not face any problem from construction works. So, no complaint has been registered by the GRCs during the reporting period.

V. FOLLOW UP ACTIONS, RECOMMENDATION AND DISCLOSURE

53. In most of the Pourashavas, project implementation works of IUGIP is ongoing. In these sub-projects addressing of social safeguard compliances considered with importance. During preparation of design for the subprojects social safeguard impacts are screened, impacts are assessed to consider the mitigation methodology and to determine requirement of preparation resettlement plan or due diligence report.

54. The baseline data are available from Social Screening report, PSSA report and Due Diligence reports. The Social safeguard team are visiting construction works ongoing projects to monitor how the social safeguard compliances are addressed during construction works. During the monitoring, the Assistant Engineer from Pourashava and Monitoring Engineer of PMDSC assist the social safeguard team of PMDSC in monitoring. The monitoring team uses prescribed monitoring checklists.

55. The team works on construction work ongoing places, workers shed and meet community people. Monitoring reports are prepared on the basis of this observation too. The data will be used in measuring the changes on social safeguard condition.

A. Mitigation of impacts and GRM management

56. IUGIP aims at enhancing urban governance and improving infrastructure sustainability of the targeted Pourashavas using an approach based on integrated and holistic planning. The Project supports the development of key urban infrastructure, focusing on projects that enhance the urban environment, poverty alleviation, gender responsive and economic development. The Project also supports the Government to strengthen Pourashavas management and capacity for effective and sustainable urban development.

57. IUGIP has developed a Grievance Redress Mechanism (GRM) to resolve or mitigate complaints of aggrieved persons. As of the end of the reporting period, construction works of only a few schemes have started, so the project beneficiaries do not face any adverse impacts from construction works. The Grievance Redress Committees (GRCs) have not received any complaint from the community people.

58. While there are no significant or no IR impacts and impacts are of short term and can easily be mitigated, the project prepares due diligence report. The PSSA reported that roads and drains will be constructed within the rights-of-way (ROW) of Pourashava roads, while improvements in low-income neighborhoods, markets, and parks will take place on Pourashava land. The initial assessment confirmed that no land acquisition, physical displacement, or permanent economic displacement of individuals, households, or communities is expected.

59. PSSA consultants assessed social safeguard impacts in the sample five Pourashavas. It was reported the RBL program activities are unlikely to have significant adverse impacts. The potential impacts are short term and can easily be mitigated. Though it was mentioned in that there are few trees in the RoWs. But during visit of the social safeguard team in 2024, no trees were found in the RoWs in the Pourashavas. The team discussed with the community people about the reported trees. Nobody claimed ownership of any trees. All of these affected trees were under Pourashava ownership. The program has plantation policy to plant multiple number of saplings at the under-construction roadside in place of an affected tree.

60. During visits of social safeguard team, local people raised some problems due to construction works which required immediate solutions to avoid losses/ difficulties of the

people. The team had to solve the problem on the spot. The community expressed their satisfaction on the solution. These actions are being followed up and ensured by the safeguard team.

61. During visit to ongoing project at Modhupur, people showed their concerns that due to road construction works and in absence of water passing facilities there are water loggings for abnormally long time. The consultants advised contractor to arrange a cross pipe drain for easy passing of water from the area. In the next visit, consultants found that a cross-pipe drain has been arranged by the contractor and there is no water logging.

62. During visit at Naria Pourashava, it was found out that construction works of drainage is ongoing and contractor stacks construction materials in front of a hospital and some shops. The contractor was advised to shift the materials to appropriate place without delay. The contractor started shifting the construction materials in presence of the social safeguard monitoring team and shifted all of the construction materials.

63. The SSMR will be submitted to the ADB for their concurrence. After clearance from the ADB, this SSMR will be disclosed in ADB and LGED Website.

B. Recommendation

- (i) Social Safeguard Training should be started soon. Lack of proper training significant benefit from the GRM is not observed.
- (ii) Addressing of social safeguard compliances have to be monitored frequently on start-up-subprojects

Appendix 1: Cumulative Physical Progress and Social Impact Assessment up to March 2024

Sl. No.	Name of District	Name of Pourashava	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
1	Faridpur	Bhanga	IUGIP/BHAN/UT/01/2023	Awarded	12.00%	12.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required. No other IR impacts. IP impacts assessed and no IP impacts found	Due Diligence Report (DDR) prepared	Work ongoing
2	Faridpur	Bhanga	IUGIP/BHAN/UT/02/2023	Awarded	1.00%	1.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required. No other IR impacts. IP impacts assessed and no IP impacts found	Due Diligence Report (DDR) prepared	Work ongoing

Sl. No.	Name of District	Name of Pourashava	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
3	Faridpur	Boalmari	IUGIP/B OAL/UT +DR/01/ 2023	Awarded	24.24%	24.24%	Social Safeguard/ Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required. No other IR impacts. IP impacts assessed and no IP impacts found	Due Diligence Report (DDR) prepared	Work ongoing
4	Faridpur	Boalmari	IUGIP/B OAL/UT +DR/02/ 2023	Awarded	30.48%	30.48%	Social Safeguard/ Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work ongoing
5	Gazipur	Kaliganj	IUGIP/K ALI/UT+	Awarded	7.00%	7.00%	Social Safeguard/ Resettlement	The subproject visited and public consultation conducted. (photo	Due Diligence Report (DDR) prepared	Work ongoing

Sl. No.	Name of District	Name of Pourashava	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
			DR/01/2023				Impact Assessments completed	provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found		
6	Gazipur	Kaliganj	IUGIP/KALI/UT+DR/02/2023	Awarded	5.29%	5.29%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required. No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work ongoing

Sl. No.	Name of District	Name of Pourashava	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
7	Gazipur	Kaliganj	IUGIP/K ALI/UT+DR/03/2023	Under proses	N/A	N/A	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required. No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Retender will be done
8	Gazipur	Kaliakoir	IUGIP/K ALIA/UT+DR/01/2023	Under proses	N/A	N/A		The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Under Evaluation

Sl. No.	Name of District	Name of Paurasaha	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
9	Gazipur	Kaliakoir	IUGIP/KALIA/UT+DR/02/2023		N/A	N/A	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Tender processing
10	Gazipur	Kaliakoir	IUGIP/KALIA/UT+DR/04/2023		N/A	N/A		The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Tender under process
11	Munshiganj	Munshiganj	IUGIP/MUNSHIG/UT+DR/01/2023	Under Process	0.00%	0.00%	Social Safeguard/Resettlement Impact	The subproject visited and public consultation conducted. (photo provided). The road and	Due Diligence Report (DDR) prepared	Work not yet started

Sl. No.	Name of District	Name of Pourashava	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
							Assessments completed	drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found		
12	Munshiganj	Munshiganj	IUGIP/MUNS/UT+DR/02/2023	Awarded	8.00%	8.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required. No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Drain work ongoing
13	Narayanganj	Araihazar	IUGIP/A RAI/UT+DR/01/2023	Awarded	12.00%	12.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava	Due Diligence Report (DDR) prepared	Work ongoing

Sl. No.	Name of District	Name of Panchayat	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
								received. No additional land required. No other IR impacts. IP impacts assessed and no IP adverse impacts found		
14	Narayanjan	Araihazar	IUGIP/A RAI/UT+ DR/02/2023	Awarded	10.00%	10.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Panchayat received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work ongoing
15	Narayanjan	Araihazar	IUGIP/A RAI/UT+ DR/04/2023	Awarded	15.00%	15.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Panchayat received. No additional land required, No other IR impacts. IP impacts	Due Diligence Report (DDR) prepared	Work ongoing

Sl. No.	Name of District	Name of Pourashava	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
								assessed and no IP adverse impacts found		
16	Narayanjanj	Araihazar	IUGIP/A RAI/UT+DR/03/2023	Under proses	N/A	N/A	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Under Evaluation, MDS 31.03.24
17	Rajbari	Goalandia	IUGIP/G OAL/UT+DR/01/2023	Awarded	20.00%	20.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work ongoing

Sl. No.	Name of District	Name of Pourohara	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
24	Narsingdi	Monohordi	IUGIP/MONO/UT+DR/01/2023	Under proses	N/A	N/A	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourohara received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	NOA (Notification of Award) Issued
25	Narsingdi	Monohordi	IUGIP/MONO/UT/01/2023	Under proses	N/A	N/A	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourohara received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Under Evaluation
26	Narsingdi	Monohordi	IUGIP/MONO/UT+DR/02/2023	Under proses	N/A	N/A	Social Safeguard/	The subproject visited and public consultation conducted. (photo provided). The road and	Due Diligence Report (DDR) prepared	Under Evaluation

Sl. No.	Name of District	Name of Pourashava	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
							Resettlement Impact Assessments completed	drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found		
27	Kishoreganj	Hossainpur	IUGIP/HOSS/UT+DR/01/2023	Under proses	2.00%	2.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work started in one road out of total 14 nos roads
28	Kishoreganj	Hossainpur	IUGIP/HOSS/DR/02/2023	Work not yet started	0.00%	0.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava	Due Diligence Report (DDR) prepared	Work not yet started

Sl. No.	Name of District	Name of Pourashava	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
								received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found		
29	Madaripur	Kalkini	IUGIP/KALK/UT+DR/01/2023	Awarded	1.00%	1.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work ongoing
30	Madaripur	Kalkini	IUGIP/KALK/UT/01/2023	Material Mobilization on-going	0.00%	0.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts	Due Diligence Report (DDR) prepared	Material Mobilization on-going

Sl. No.	Name of District	Name of Pourashava	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
								assessed and no IP adverse impacts found		
31	Madaripur	Kalkini	IUGIP/KALK/UT/02/2023	Contract Signed, work not yet started	0.00%	0.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Contract Signed, work not yet started
32	Tangail	Madhupur	IUGIP/MADH/UT+DR/01/2023	Awarded	6.21%	6.21%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work ongoing

Sl. No.	Name of District	Name of Panchayat	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
33	Tangail	Madhupur	IUGIP/M ADH/UT/01/2023	Awarded	19.62%	19.62%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Panchayat received. No additional land required. No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work ongoing
34	Tangail	Madhupur	IUGIP/M ADH/UT/03/2023	Awarded	10.35%	10.35%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Panchayat received. No additional land required. No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work ongoing
35	Tangail	Madhupur	IUGIP/M ADH/UT +DR/02/2023	Work not yet started	0.00%	0.00%	Social Safeguard/Resettlement Impact	The subproject visited and public consultation conducted. (photo provided). The road and	Due Diligence Report (DDR) prepared	Work not yet started

Sl. No.	Name of District	Name of Paurashava	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
							Assessments completed	drain will be constructed on municipal own land. No-objection certificate from Paurashava received. No additional land required. No other IR impacts. IP impacts assessed and no IP adverse impacts found		
36	Brahmanbaria	Brahmanbaria	IUGIP/BRUH/UT+DR/01/2023	Awarded	6.00%	6.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Paurashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work ongoing
37	Brahmanbaria	Brahmanbaria	IUGIP/BRUH/UT+DR/02/2023	Work started on 26-Mar-24	0.00%	0.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Paurashava	Due Diligence Report (DDR) prepared	Work started on 26-Mar-24

Sl. No.	Name of District	Name of Paurasaha	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
								received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found		
38	Brahmanbaria	Brahmanbaria	IUGIP/BRAH/UT+DR/03/2023	Under Process	0.00%	0.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work not yet started
39	Chattogram	Sandwip	IUGIP/SAND/UT+DR/01/2023	Site Mobilization Ongoing	2.00%	2.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts	Due Diligence Report (DDR) prepared	Site Mobilization Ongoing

Sl. No.	Name of District	Name of Pourashava	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
								assessed and no IP adverse impacts found		
40	Chattagram	Sandwip	IUGIP/S AND/UT/01/2023	Under Process	N/A	N/A	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required. No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	NoA Issued
41	Chattagram	Banskhal	IUGIP/BANS/UT+DR/01/2023	Awarded	12.00%	12.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required. No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work ongoing

Sl. No.	Name of District	Name of Pourashava	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
42	Chattagram	Banskhal	IUGIP/BANS/UT+DR/02/2023	Awarded	9.50%	9.50%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required. No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work ongoing
43	Chattagram	Banskhal	IUGIP/BANS/UT+DR/03/2023		N/A	N/A	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required. No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Tender process ongoing

Sl. No.	Name of District	Name of Paurasaha	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
44	Chattagram	Chandanaish	IUGIP/C HAN/UT/01/2023	Under Process	N/A	N/A	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Paurashava received. No additional land required. No other IR impacts. IP impacts assessed and no IP adverse impacts found		NOA Issued
45	Chattagram	Chandanaish	IUGIP/C HAN/UT/02/2023	Under Process	N/A	N/A	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Paurashava received. No additional land required. No other IR impacts. IP impacts assessed and no IP adverse impacts found		NOA Issued
46	Chattagram	Raozan	IUGIP/RAOZ/UT+DR/01/2023	Contract just signed, Work not	0.00%	0.00%	Social Safeguard/Resettlement Impact	The subproject visited and public consultation conducted. (photo provided). The road and	Due Diligence Report (DDR) prepared	Contract just signed,

Sl. No.	Name of District	Name of Pourashava	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
				yet started			Assessments completed	drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required. No other IR impacts. IP impacts assessed and no IP adverse impacts found		Work not yet started
47	Chattagram	Raozan	IUGIP/R AOZ/MF/01/2023	Retender, Evaluation, MDS 01-Apr-24	N/A	N/A	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Retender, Evaluation, MDS 01-Apr-24
48	Chattagram	Raozan	IUGIP/R AOZ/UT/02/2023	Under Process	N/A	N/A	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava	Due Diligence Report (DDR) prepared	Retender, Evaluation

Sl. No.	Name of District	Name of Pourashava	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
								received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found		
49	Chandpur	Haziganj	IUGIP/H AZI/UT+DR/01/2023	Awarded	26.00%	26.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work ongoing
50	Chandpur	Haziganj	IUGIP/H AZI/DR/01/2023	Awarded	5.00%	5.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts	Due Diligence Report (DDR) prepared	Work ongoing

Sl. No.	Name of District	Name of Pourashava	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
								assessed and no IP adverse impacts found		
51	Chandpur	Haziganj	IUGIP/H AZI/DR/04/2023	Awarded	3.00%	3.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work ongoing
52	Chandpur	Matlab	IUGIP/M ATL/UT+DR/01/2023	Awarded	16.00%	16.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work ongoing

Sl. No.	Name of District	Name of Pourashava	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
53	Chandpur	Matlab	IUGIP/MATL/UT+DR/02/2023	Awarded	12.00%	12.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work ongoing
54	Chandpur	Faridganj	IUGIP/FARI/UT+DR/02/2023	Work not yet started	0.00%	0.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work not yet started
55	Chandpur	Faridganj	IUGIP/FARI/UT/01/2023	Work not yet started	0.00%	0.00%	Social Safeguard/Resettlement Impact	The subproject visited and public consultation conducted. (photo provided). The road and	Due Diligence Report (DDR) prepared	Work not yet started

Sl. No.	Name of District	Name of Pourashava	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
							Assessments completed	drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found		
56	Feni	Sonagazi	IUGIP/SONA/UT+DR/01/2023	Mobilization on-going	0.00%	0.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Mobilization on-going
57	Feni	Sonagazi	IUGIP/SONA/UT+DR/02/2023	Tender received, under Evaluation	N/A	N/A	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava	Due Diligence Report (DDR) prepared	Tender received, under Evaluation

Sl. No.	Name of District	Name of Paurasaha	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
								received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found		
58	Khagrichori	Khagrichori	IUGIP/KHAG/UT+DR/01/2023	Awarded	56.25%	56.25%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work ongoing
59	Khagrichori	Khagrichori	IUGIP/KHAG/UT+DR/02/2023	Awarded	36.49%	36.49%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts	Due Diligence Report (DDR) prepared	Work ongoing

Sl. No.	Name of District	Name of Paurasaha	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
								assessed and no IP adverse impacts found		
60	Khagrac hori	Khagrac hori	IUGIP/K HAG/UT +DR/03/ 2023	Awarded	40.00%	40.00%	Social Safeguard/ Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work ongoing
61	Khagrac hori	Khagrac hori	IUGIP/K HAG/UT +DR/04/ 2023	Under Evaluation	N/A	N/A	Social Safeguard/ Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Under Evaluation

Sl. No.	Name of District	Name of Pourashava	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
62	Bandarban	Bandarban	IUGIP/BAND/UT+DR/01/2023	Awarded	N/A	N/A	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Under Evaluation
63	Noakhali	Chowmuhani	IUGIP/C HOW/UT+DR/01/2023	Awarded	6.00%	6.00%	Social Safeguard/Resettlement Impact Assessments completed	Sub-project visited and social screening done. It was found out that four roadside temporary floating business person will be affected and loss of their income is identified. No other IR or IP adverse impact assessed.	Social safeguards document will be updated for ADB's review. This document will be reflected in the next SSMR.	Work ongoing
64	Noakhali	Chowmuhani	IUGIP/C HOW/UT/01/2023	Awarded	15.00%	15.00%	Social Safeguard/Resettlement Impact	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed	Due Diligence Report (DDR) prepared	Work ongoing

Sl. No.	Name of District	Name of Paurashava	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
							Assessments completed	on municipal own land. No-objection certificate from Paurashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found		
65	Noakhali	Chowmahani	IUGIP/C HOW/UT/03/2023	Retender + Evaluation	N/A	N/A	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Paurashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Retender+ Evaluation
66	Laxmipur	Raipur	IUGIP/R AIP/UT/01/2023	Work not yet started	0.00%	0.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Paurashava received. No additional	Due Diligence Report (DDR) prepared	Work not yet started

Sl. No.	Name of District	Name of Paurasaha	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
								land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found		
67	Laxmi pur	Raipur	IUGIP/R AIP/UT+ DR/03/2023	Material Mobilization on-going	0.00%	0.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Material Mobilization on-going
68	Habiganj	Chunarughat	IUGIP/C HUN/UT/01/2023	Awarded	1.00%	1.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work Ongoing

Sl. No.	Name of District	Name of Paurasaha	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
69	Habiganj	Chunarughat	IUGIP/C HUN/UT +DR/01/2023	Awarded	4.62%	4.62%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work Ongoing
70	Habiganj	Chunarughat	IUGIP/C HUN/UT/02/2023	Awarded	0.00%	0.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work not yet started
71	Moulavibazar	Kulaura	IUGIP/K ULA/UT +DR/01/2023	Work not yet started	0.00%	0.00%	Social Safeguard/Resettlement Impact	The subproject visited and public consultation conducted. (photo provided). The road and	Due Diligence Report (DDR) prepared	Work not yet started

Sl. No.	Name of District	Name of Pourashava	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
							Assessments completed	drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found		
72	Moula vibazar	Kulaura	IUGIP/KULA/UT+DR/03/2023	Contract just signed, Work not yet started	0.00%	0.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Contract just signed, Work not yet started
73	Moula vibazar	Kulaura	IUGIP/KULA/UT+DR/05/2023	Contract to be signed 15.Apr-2024	0.00%	0.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava	Due Diligence Report (DDR) prepared	Contract to be signed 15.Apr-2024

Sl. No.	Name of District	Name of Panchayat	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
								received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found		
74	Moulvibazar	Moulvibazar	IUGIP/MOUL/UT+DR/01/2023	Awarded	10.00%	10.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Panchayat received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work Ongoing
75	Moulvibazar	Moulvibazar	IUGIP/MOUL/UT+DR/02/2023	Awarded	2.00%	2.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Panchayat received. No additional land required, No other IR impacts. IP impacts	Due Diligence Report (DDR) prepared	Work started

Sl. No.	Name of District	Name of Pourashava	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
								assessed and no IP adverse impacts found		
76	Kustia	Bheramara	IUGIP/BER/UT+DR/01/2023	Awarded	22.00%	22.00%	Social Safeguard/Resettlement Impact Assessments completed		Due Diligence Report (DDR) prepared	Work Ongoing
77	Kustia	Bheramara	IUGIP/BER/UT+DR/04/2023	Awarded	25.00%	25.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work Ongoing
78	Kustia	Bheramara	IUGIP/BER/UT+DR/02/2023	Awarded	N/A	N/A	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava		Under Evaluation

Sl. No.	Name of District	Name of Paurasaha	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
								received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found		
79	Kustia	Kumarkhali	IUGIP/KUMA/UT+DR/01/2023	Awarded	12.00%	12.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Paurashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work Ongoing
80	Kustia	Kumarkhali	IUGIP/KUMA/UT+DR/02/2023	Under Evaluation	N/A	N/A	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Paurashava received. No additional land required, No other IR impacts. IP impacts	Due Diligence Report (DDR) prepared	Under Evaluation

Sl. No.	Name of District	Name of Pourashava	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
								assessed and no IP adverse impacts found		
81	Kustia	Kumarkhali	IUGIP/KUMA/UT+DR/03/2023	Under Evaluation	N/A	N/A	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found		Under Evaluation
82	Meherpur	Gangni	IUGIP/GANG/UT+DR/01/2023	Awarded	20.00%	20.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work Ongoing

Sl. No.	Name of District	Name of Pourashava	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
83	Meherpur	Gangni	IUGIP/GANG/MF/01/2023	Awarded	0.00%	0.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work not yet started
84	Meherpur	Gangni	IUGIP/GANG/UT/01/2023	Under Evaluation	N/A	N/A	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Under Evaluation
85	Meherpur	Gangni	IUGIP/GANG/MF/02/2023	Under Evaluation		N/A	Social Safeguard/Resettlement Impact	The subproject visited and public consultation conducted. (photo provided). The road and		Under Evaluation

Sl. No.	Name of District	Name of Pourashava	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
					N/A		Assessments completed	drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	
86	Chudanga	Alomdanga	IUGIP/LAM/UT+DR/01/2023	Awarded	28.00%	28.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work Ongoing
87	Jashore	Keshobpur	IUGIP/KE/SH/UT+DR/01/2023	Awarded	15.00%	15.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava	Due Diligence Report (DDR) prepared	Work Ongoing

Sl. No.	Name of District	Name of Paurasava	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
								received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found		
88	Jashore	Keshobpur	IUGIP/KESH/UT/01/2023	Awarded	3.00%	3.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work Ongoing
89	Jashore	Keshobpur	IUGIP/KESH/MF/01/2023	Under Process	N/A	N/A	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts	Due Diligence Report (DDR) prepared	NOA Issued

Sl. No.	Name of District	Name of Pourashava	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
								assessed and no IP adverse impacts found		
90	Jashore	Keshobpur	IUGIP/KESH/UT/02/2023	Under Process	0.00%	0.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Contract Signed
91	Pabna	Santhia	IUGIP/SANT/UT+DR/01/2023	Awarded	16.38%	16.38%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work Ongoing

Sl. No.	Name of District	Name of Pourashava	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
92	Pabna	Santhia	IUGIP/S ANT/UT/01/2023	Awarded	16.50%	16.50%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work Ongoing
93	Pabna	Santhia	IUGIP/S ANT/MF/01/2023	Tender received, under Evaluation	N/A	N/A	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Tender received, under Evaluation
94	Rajshahi	Naohata	IUGIP/N AOH/UT/01/2023	Awarded	32.00%	32.00%	Social Safeguard/Resettlement Impact	The subproject visited and public consultation conducted. (photo provided). The road and	Due Diligence Report (DDR) prepared	Work ongoing

Sl. No.	Name of District	Name of Paurashava	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
							Assessments completed	drain will be constructed on municipal own land. No-objection certificate from Paurashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found		
95	Rajshahi	Naohata	IUGIP/N AOH/UT +DR/01/ 2023	Awarded	1.00%	1.00%	Social Safeguard/ Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Paurashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work ongoing
96	Rajshahi	Bhawani ganj	IUGIP/B HAW/UT +DR/01/ 2023	Awarded	5.00%	5.00%	Social Safeguard/ Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Paurashava	Due Diligence Report (DDR) prepared	Work ongoing

Sl. No.	Name of District	Name of Paurasava	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
								received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found		
97	Rajshahi	Bhawani ganj	IUGIP/B HAW/UT /01/2023	Under Process	0.00%	0.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Contract just signed, Work not yet started
98	Rajshahi	Bhawani ganj	IUGIP/B HAW/UT /02/2023	Under Evaluation	N/A	N/A	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts	Due Diligence Report (DDR) prepared	Under Evaluation

Sl. No.	Name of District	Name of Pourashava	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
								assessed and no IP adverse impacts found		
99	Chapai Nawabganj	Rohanpur	IUGIP/R OHA/UT +DR/02/2023	Awarded	23.00%	23.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work ongoing
100	Chapai Nawabganj	Rohanpur	IUGIP/R OHA/UT/01/2023	Awarded	21.15%	21.15%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work ongoing

Sl. No.	Name of District	Name of Pourashava	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
101	Chapai Nawabganj	Rohanpur	IUGIP/ROHA/MF/01/2023	Under Process	0.00%	0.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Contract just signed, work not yet started
102	Kurigram	Ulipur	IUGIP/ULIP/UT+DR/01/2023	Awarded	15.00%	15.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work ongoing
103	Kurigram	Ulipur	IUGIP/ULIP/UT/01/2023	Awarded	10.11%	10.11%	Social Safeguard/Resettlement Impact	The subproject visited and public consultation conducted. (photo provided). The road and		Work ongoing

Sl. No.	Name of District	Name of Pourashava	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
							Assessments completed	drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	
104	Lalmoinirhat	Patgram	IUGIP/PATG/UT+DR/01/2023	Awarded	0.00%	0.00%	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found	Due Diligence Report (DDR) prepared	Work not yet started
105	Lalmoinirhat	Patgram	IUGIP/PATG/UT+DR/02/2023	Under Evaluation	N/A	N/A	Social Safeguard/Resettlement Impact Assessments completed	The subproject visited and public consultation conducted. (photo provided). The road and drain will be constructed on municipal own land. No-objection certificate from Pourashava	Due Diligence Report (DDR) prepared	Under Evaluation

Sl. No.	Name of District	Name of Pourashava	Package No.	Status of Contract Award	Physical Progress During the Reporting period	Cumulative Physical Progress up to March 2024	Nature of Social Safeguard/Resettlement Impact	Brief summary/details of Land Acquisition and Involuntary Resettlement and TMRESC/IP safeguards assessment	Nature of document prepared	Remarks
								received. No additional land required, No other IR impacts. IP impacts assessed and no IP adverse impacts found		
			TOTAL		10.64%	10.64%				

Note: Out of 105 Packages in the table above, 104 packages were visited and social safeguard impacts on these packages were assessed during PPTA (Project Preparatory Technical Assistance) period of IUGIP. In this period, safeguard consultants found 4 temporary business persons will be affected at IUGIP/CHOW/UT+DR/01/2023 under Chowmuhan Pourashava. As their source of income would be affected due to project construction works, proper due diligence should be undertaken and accordingly, appropriate social safeguards document will be prepared. Among the five selected pourashavas for PSSA, Chowmuhan was one of the sample subprojects. During the reporting period, 4 subprojects were visited by Resettlement / social safeguard team of PMDSC of IUGIP and they screened the subprojects. The sub-projects are IUGIP/KALIA/ UT+DR/04/2023 under Kaliakoir Pourashava, IUGIP/MUNS/UT + DR/02/2023 under Mirkadim Pourashava, IUGIP/NAZI/UY +DR/01/2023 and IUGIP/NAZI/UY +DR/02/2023 under Nazirhat Pourashava. Resettlement Specialists of PMDSC prepared three due diligence reports during the reporting period and submitted to PMU. As the Resettlement/ Social safeguard specialists received clearance for one DDR (IUGIP/KALIA/UT+DR/04/2023) from the PMU during the reporting period, information of only one number of impacts assessed subproject has been mentioned in the above table. After the reporting period, Resettlement/ Social safeguard specialist received clearance for the rest submitted DDRs. DDRs are submitted to PMU by the MDS Consultants. Disclosure of DDRs in the LGED/Project website is under process. The disclosure links will be provided in the next semi-annual social safeguard monitoring report.

Appendix 2: Photo of Public Consultations conducted by Social Safeguards Team in different Pourashavas



Photos of Public consultations and attendance of the participants



Public Consultation Meeting (PCM) at Sundorganj pourashava,
Total Participants - 17 Male- 17 Female-0

**Improving Urban Governance and Infrastructure Program (IUGIP)
Focus Group Discussions (FGD)
for
Environmental & Social Safeguards**

Name of Pourashava: Sundargang
Location: Mingonj Bazar

District: Gaibandha
Word no: 01

Meeting Date: 27-3-2024

List of Participants

SL No.	Name	Mobile Number	Occupation	Signature
1	ডাঃ মাহবুব রশীদ	01712661920	Mayor	[Signature]
2	মোঃ হুমায়ুন হোসেন	01637-760933		[Signature]
3	মোঃ নূরুজ্জামান	01717-538561		[Signature]
4	ডাঃ মোহাম্মদ মোহাম্মদ			
5	ডাঃ হুমায়ুন হোসেন	0171762478	সহকারী সিটিং	[Signature]
6	মোঃ হুমায়ুন হোসেন	01305892191	সহকারী	[Signature]
7	মোঃ হুমায়ুন হোসেন	01706320702		[Signature]
8	মোঃ হুমায়ুন হোসেন	01730968360		[Signature]
9	মোঃ হুমায়ুন হোসেন	01732803056		[Signature]
10	মোঃ হুমায়ুন হোসেন	01713864937		[Signature]
11	মোঃ হুমায়ুন হোসেন	01714909402		[Signature]
12	মোঃ হুমায়ুন হোসেন	01788-153814		[Signature]
13	মোঃ হুমায়ুন হোসেন			[Signature]
14	মোঃ হুমায়ুন হোসেন			[Signature]
15	মোঃ হুমায়ুন হোসেন	01750882987		[Signature]
16	মোঃ হুমায়ুন হোসেন			[Signature]
17	Md. Mizanur Rahman	01725903288	Jr. Res. Specialist	[Signature]



Public Consultation Meeting (PCM) at Bandarban pourashava
Total Participants - 15 Male- 07 Female-08

Local Government Engineering Department (LGED)
Improving Urban Governance and Infrastructure Program (IUGIP)
Focus Group Discussion (FGD) for Resettlement and Social Safeguard (Proposed Schemes)

Name of Pourashava : Bandarban Date: 09.05.24
 Location: Uzanipar
 Word No: 05

Attendance Sheet

S/N	Name of Participant	Designation	Mobile No	Signature
1	Mong Mong Sing	Counselor	01558123174	
2	A May Ching	counselor	01556508671	
3	May Hai Nue	H. wife	01632630685	
4	Wong Sue Thui	"	01871165578	
5	Nasima Akter	"	01856471128	
6	Nitu Barua	"	01554805562	
7	Mong Sa Nu	BUS	01556581263	
8	Moung to	social worker	01575059650	
9	Bindu Chandra Das	"	01556742949	
10	Ranjit Das	"	01828949482	
11	Badal Das	BUS	01819085559	
12	Nue Yai Ching	H. wife	01552871693	
13	Pruu May	"	01861627845	
14	Hteu Nue Ching	"	01523037096	
15	Nwe Nahar	"	01310791360	



Public Consultation Meeting (PCM) at Chhatak pourashava
Total Participants – 11, Male- 05 Female-06

Improving Urban Governance and Infrastructure Program (IUGIP)
Focus Group Discussions (FGD) for Social and environmental Safeguard

Name of Pourashava: Chhatak
Location: Labourer para
Meeting Date: 06.03.2024

District: Sunamganj
Time: 1.40 PM

List of Participants

SL	Name	Mobile Number	Occupation	Signature
১.	শ্রী: জাহাঙ্গীর আলী	০১৭৭৪৭৭৬৭৩	ভূমি	[Signature]
২.	শ্রী: তাজিন আহমেদ	০১৭৭৭৩৭৭৩১	চাকরি	[Signature]
৩.	শ্রী: তানজিনা আক্তার ইমি	০১৭০৩০০৪৩২৫	ছাত্রী	ইমি
৪.	তানিয়া আক্তার	H	ছাত্রী	তানিয়া
৫.	হাবিয়া	H	ছাত্রী	হাবিয়া
৬.	আব্বাস আক্তার	H	ছাত্রী	আব্বাস
৭.	সম্মত রায়	-	ছাত্রী	সম্মত
৮.	শ্রী: সফিয়ার হোসেন	০১৭৩২৭২৬৫১৭	চাকরি	সফিয়ার হোসেন
৯.	শ্রী: ফাহিমাহ মিয়া	০১৭৪৭২২৪৪৭	ছাত্রী	ফাহিমাহ মিয়া
১০.	শ্রী: শাহানা	০১৬৪৫৩৩৩২৩	ভূমি	শাহানা
১১.	শ্রী: মদন কান্ত	-	চাকরি	মদন



Public Consultation Meeting (PCM) at Nazirhat pourashava
Total Participants - 15 Male- 13 Female-02

Local Government Engineering Department (LGED)
Improving Urban Governance and Infrastructure Program (IUGIP)

Public consultation meeting for environmental & social safeguards (Proposed schemes)

Pourashava Name: Nazirhat

Date: 03.03.2024

Location: E. Forhadabad

Ward no: 09

Attendance Sheet

Sl. No.	Name of Participant	Designation/Service	Mobile no.	Signature	Remarks
1	md. Soliman	Counsellor	01822817171	[Signature]	
2	Hasina montaj	"	01825142813	[Signature]	
3	md. Yakob	Bus.	0181170611	[Signature]	
4	md. Kamal	"	01856011582	[Signature]	
5	Sofiul Atom	Dr.	01818670846	[Signature]	
6	Homann Kabir	Bus.	01829290432	[Signature]	
7	Zeatul	"	01316381570	[Signature]	
8	Samonara	"	01814318862	[Signature]	
9	Anwar Hossin	"	01817771566	[Signature]	
10	Abdur Rahim	Imam	01815623184	[Signature]	
11	Azzad	Bus.	01890482405	[Signature]	
12	Itlaque Hossin	"	0181208232	[Signature]	
13	Mahbubul Alam	sewage	01832579660	[Signature]	
14	Mossada Akter	H. wife	01891630953	[Signature]	
15	Jenu Akter	H. wife	01824314241	[Signature]	



Public Consultation Meeting (PCM) at Dhaganbhuyan pourashava
Total Participants - 15 Male- 10 Female-05

Local Government Engineering Department (LGED)
Improving Urban Governance And Infrastructure Program (IUGIP)
Public consultation meeting for environmental & social safeguards (proposed schemes)

Pourashava name: Daganbhuyan Date: 05.03.2024
Location: Badarpur
Ward No: 07

Sl no	Name of Participant	Designation /Service	Mobile No	Signature	Rem
1	Kazi Sakawat Hossain	XEN	01819838176	[Signature]	
2	Obaidul Hossain	W.A	01816246323	[Signature]	
3	Abu Tarik	SAE	01712018671	[Signature]	
4	Kamrul Hasan	counselor	01715738179	[Signature]	
5	Afser Uddin	Bus.	01819672075	[Signature]	
6	Ismail Hossain	"	01817400603	[Signature]	
7	Obaidul	"	01715070895	[Signature]	
8	Hanif	Agg.	01830015971	[Signature]	
9	Safiq Ullah	"	01832983701	[Signature]	
10	Shah Alam	"	01856228978	[Signature]	
11	Nasima	H. wife	01832375120	[Signature]	
12	Brenty Akter	"	DO	[Signature]	
13	Aysha Khatun	"	01819795424	[Signature]	
14	Towbar Nesa	"	-	[Signature]	
15	Zosna Ara	"	-	[Signature]	



Public Consultation Meeting (PCM) at Mirkadim pourashava
Total Participants - 15 Male- 11 Female-04

Local Government Engineering Department (LGED)
Improving Urban Governance and Infrastructure Program (IUGIP)

Public consultation meeting for environmental & social safeguards (Proposed schemes)

Pourashava Name: Mirkadim Date: 30.01.24
Location: Sudarchar Temple in compound
Ward no: 09

Attendance Sheet

SL no	Name of Participant	Designation/ Service	Mobile no	Signature	Remarks
1	<u>গোবিন্দ চন্দ্র</u>	<u>সহকারী</u>	<u>018234500</u>	<u>[Signature]</u>	
2	<u>সামসি (কো)</u>	<u>ন</u>		<u>[Signature]</u>	
3	<u>জাহাঙ্গীর মল্লিক</u>	<u>সহকারী</u>	<u>01956-02050</u>	<u>[Signature]</u>	
4	<u>শ্রী: সারথী</u>	<u>সহকারী</u>	<u>01722788000</u>	<u>[Signature]</u>	
5	<u>সুজা সারথী</u>	<u>সহকারী</u>	<u>01739315501</u>	<u>[Signature]</u>	
6	<u>কমলা কান্ত মল্লিক</u>	<u>সহকারী</u>	<u>0177958867</u>	<u>[Signature]</u>	
7	<u>সাবিত্রী মল্লিক</u>	<u>সহকারী</u>	<u>01206000000</u>	<u>[Signature]</u>	
8	<u>সুজা সারথী</u>	<u>সহকারী</u>	<u>01460167776</u>	<u>[Signature]</u>	
9	<u>সাবিত্রী মল্লিক</u>	<u>সহকারী</u>	<u>01936020990</u>	<u>সাবিত্রী</u>	
10	<u>সাবিত্রী মল্লিক</u>	<u>সহকারী</u>	<u>01866946641</u>	<u>[Signature]</u>	
11	<u>সাবিত্রী মল্লিক</u>	<u>সহকারী</u>	<u>01913130005</u>	<u>সাবিত্রী</u>	
12	<u>সাবিত্রী মল্লিক</u>	<u>সহকারী</u>	<u>01931920934</u>	<u>সাবিত্রী</u>	
13	<u>সাবিত্রী মল্লিক</u>	<u>সহকারী</u>	<u>01733991672</u>	<u>[Signature]</u>	
14	<u>সাবিত্রী মল্লিক</u>	<u>সহকারী</u>	<u>014464428</u>	<u>[Signature]</u>	
15	<u>সাবিত্রী মল্লিক</u>	<u>সহকারী</u>	<u>01406747459</u>	<u>সাবিত্রী</u>	



Public Consultation Meeting (PCM) at Kaliakair pourashava
Total Participants - 10 Male- 10 Female-0

Improving Urban Governance and Infrastructure Project (IUGIP)
Project Readiness Services (PRS)
Public Consultation Meeting for Social Safeguards

Name of Pourashava:.....KALIKAIR.....District:.....GAZIPUR.....
Location: CONSULTANT'S OFFICE, ROAD NO-2
Meeting Date: 30.01.2024 Time: 05.30PM

List of Participants

Sl No	Name	Cell Phone Number	Age	Occupation	Signature
01	শ্রীঃ মাহমুদ হোসেন	০১৭৩৭৫৬২৭৬৮	৪২	কলিকাইর	Uttal
02	শ্রীঃ মাহমুদ হোসেন	০১৬৭০১১৬৮৮৭	৪৩	কলিকাইর	Uttal
03	শ্রীঃ মাহমুদ হোসেন	০১৬২০০২০৮৮		"	Uttal
04	শ্রীঃ মাহমুদ হোসেন	০১৭২৬৬৬৮০৮	৩৬	"	Uttal
05	শ্রীঃ মাহমুদ হোসেন	০১৭১৯৮৮৭৭৭		"	Uttal
06	শ্রীঃ মাহমুদ হোসেন	০১৭১১৭৭৫৮৭	৩২	"	Uttal
07	শ্রীঃ মাহমুদ হোসেন	০১৭৭১৩৫১১৩৬	৩০	"	Uttal
08	শ্রীঃ মাহমুদ হোসেন	০১৭৭৬৮৩৬১৫২		"	Uttal
09	শ্রীঃ মাহমুদ হোসেন	০১৭৮০৭৭৩৭৬১		"	Uttal
10	শ্রীঃ মাহমুদ হোসেন	০১৬৮৮১২৭২৩৮	২৬	"	Uttal
